

Annual Development Plan - 2024

Provincial Specific Development Grant (PSDG)

Ministry of Local Government

Final Payment Recommended

| | | | | | | |
|----|----------------------------|-------|--|---------------------------|-------|--|
| 01 | Sector | | Housing | | | |
| 02 | Location | | Jaffna | | | |
| 03 | Source of fund | | PSDG | | 03 | |
| 04 | Name of the Beneficiary | | Construction of new house (Mr. Selvan Mokan, Puttur West, Kalaimathi Veethy) | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 14.03.2024 | | | |
| 10 | Date of Completion | | 08.10.2024. | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 2.60 | | | |
| 13 | Contract Amount | | 1.80 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 1.80 | Expenditure (Rs in Mn) | 2024 | |
| | | Total | | | Total | |
| 16 | Remarks | | Work completed. Final payment Recommended Rs 100,000.00 | | | |



Last Updated - 08.10.2024

| 01 | Sector | | Housing | | | |
|----|----------------------------|-------|--|---------------------------|-------|--|
| 02 | Location | | Jaffna | | | |
| 03 | Source of fund | | PSDG | | 05 | |
| 04 | Name of the Beneficiary | | Construction of New House Mrs.kandeparasa Laksotha. Thellipali east, Thellipalai | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 14.03.2024 | | | |
| 10 | Date of Completion | | 30.11.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 2.065 | | | |
| 13 | Contract Amount | | 1.800 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 1.800 | Expenditure (Rs in Mn) | 2024 | |
| | | Total | | | Total | |
| 16 | Remarks | | Work completed. Final Payment Recommended Rs 100,000.00 | | | |



Last Updated -30.11.2024

| 01 | Sector | | Housing | | | |
|----|----------------------------|-------|--|---------------------------|-------|--|
| 02 | Location | | Jaffna | | | |
| 03 | Source of fund | | PSDG | | 08 | |
| 04 | Name of the Beneficiary | | Construction of new house (Mr.Theiventhiram Kopinath, Alangulai North, Sandilipay) | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 14.03.2024 | | | |
| 10 | Date of Completion | | 11.10.2024 | | | |
| 11 | Imprest Confimed | | | | | |
| 12 | TEC (Mn) | | 2.065 | | | |
| 13 | Contract Amount | | 2.065 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 1.800 | Expenditure (Rs in Mn) | 2024 | |
| | | Total | | | Total | |
| 16 | Remarks | | Work Completed. And Final payment Recommended Rs.100,000.00 | | | |



Last Updated - 11.10.2024

| 01 | Sector | | Housing | | | |
|----|----------------------------|-------|---|------------------------|-------|--|
| 02 | Location | | Jaffna | | | |
| 03 | Source of fund | | PSDG | | 09 | |
| 04 | Name of the Beneficiary | | Construction of new house (Mr.Stanislas Panas Parance, Kadarkarai Veethi, Passaiyoor) | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 14.03.2024 | | | |
| 10 | Date of Completion | | 29.11.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 2.065 | | | |
| 13 | Contract Amount | | 1.800 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 1.800 | Expenditure (Rs in Mn) | 2024 | |
| | | Total | | | Total | |
| 16 | Remarks | | Work Completed. Final Payment recommended Rs 100,000.00 | | | |



Last Updated - 29.11.2024

| 01 | Sector | | Housing | | | |
|----|----------------------------|-------|--|------------------------|-------|---|
| 02 | Location | | Jaffna | | | |
| 03 | Source of fund | | PSDG | | 11 | |
| 04 | Name of the Beneficiary | | Mrs.Sivamoky Sasiruban | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | Repair of House | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 14.03.2024 | | | |
| 10 | Date of Completion | | 04.07.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 4.87 | | | |
| 13 | Contract Amount | | 4.87 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 4.50 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work completed. Final Payment Recommended Rs 150000.00 | | | |



Last Updated - 04.07.2024

| 01 | Sector | | Housing | | | |
|----|----------------------------|-------|---|------------------------|-------|--|
| 02 | Location | | Mullaitivu | | | |
| 03 | Source of fund | | PSDG | | 15 | |
| 04 | Name of the Beneficiary | | Construction of new house (Mr.Mahathevan Mathikaran, Kokkuthoduvai North, Kokkuthoduvai | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 14.03.2024 | | | |
| 10 | Date of Completion | | 03.12..2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 2.06 | | | |
| 13 | Contract Amount | | 2.06 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 1.80 | Expenditure (Rs in Mn) | 2024 | |
| | | Total | | | Total | |
| 16 | Remarks | | Work Completed. Final Payment Recommended Rs . 100,000.00 | | | |




Last Updated - 03.12..2024

| 01 | Sector | | Housing | | | |
|----|----------------------------|-------|--|------------------------|-------|--|
| 02 | Location | | Mullaitivu | | | |
| 03 | Source of fund | | PSDG | | 16 | |
| 04 | Name of the Beneficiary | | Construction of new house (Mr.Makeswaran Suventhiran, Kokkuthoduvai North, Kokkuthoduvai | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 14.03.2024 | | | |
| 10 | Date of Completion | | 03.12.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 2.06 | | | |
| 13 | Contract Amount | | | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 1.80 | Expenditure (Rs in Mn) | 2024 | |
| | | Total | | | Total | |
| 16 | Remarks | | Work Completed. Final Payment Recommendation Rs. 100,000.00 | | | |



Last Updated -03.12.2024

| 01 | Sector | | Housing | | | |
|----|----------------------------|-------|--|------------------------|-------|--|
| 02 | Location | | Mannar | | | |
| 03 | Source of fund | | PSDG | | 20 | |
| 04 | Name of the Beneficiary | | Construction of new house (Mr.Parunanthu Jeyakumaran, Naruvilikulam, Kottaikadu) | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 14.03.2024 | | | |
| 10 | Date of Completion | | 03.10.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 2.065 | | | |
| 13 | Contract Amount | | 2.065 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 1.800 | Expenditure (Rs in Mn) | 2024 | |
| | | Total | | | Total | |
| 16 | Remarks | | Work Completed . Final Payment Recommended Rs. 100,000.00 | | | |

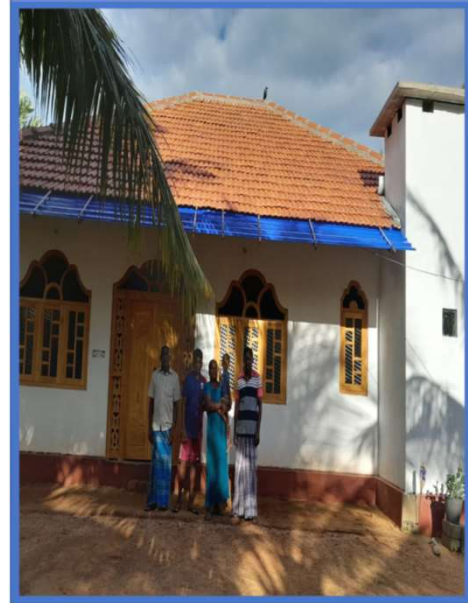

Last Updated - 03.10.2024

| 01 | Sector | | Local Authority Road | | | |
|----|----------------------------|-------|--|------------------------|-------|---|
| 02 | Location | | Jaffna | | | |
| 03 | Source of fund | | PSDG | | 02 | |
| 04 | Name of the Activity | | Construction of Vankalavadi Veethy at Nainathivu- Velanai PS | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 01.12.2023 | | | |
| 10 | Date of Completion | | 21.01.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 7.000 | | | |
| 13 | Contract Amount | | 1.545 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 1.566 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed. Final Payment recommended Rs.1530159.00 | | | |

Before



After



Last Up date 11.10.2024

| 01 | Sector | | Local Authority Road | | | |
|----|----------------------------|-------|--|------------------------|-------|---|
| 02 | Location | | Jaffna | | | |
| 03 | Source of fund | | PSDG | | 03 | |
| 04 | Name of the Activity | | Reconstruction of Cemetery Road at Watharawatthai -Valikamam East PS | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 21.06.2024 | | | |
| 10 | Date of Completion | | 07.09.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 10.000 | | | |
| 13 | Contract Amount | | 10.000 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 10.000 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work completed Final Payment recommended Rs 6,263,994.44 | | | |



Last Updated -07.09.2024

| 01 | Sector | | Local Authority Road | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 02 | Location | | Jaffna | | | |
| 03 | Source of fund | | PSDG | | 04 | |
| 04 | Name of the Activity | | Reconstruction of salambai Veethy, Pululy, Point Pedro veethy | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 05.07.2024 | | | |
| 10 | Date of Completion | | 02.09.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 2.000 | | | |
| 13 | Contract Amount | | 1.421 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 2.000 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed and .Final Payment Recommended Rs 406,930.00 | | | |



Last Updated -30.09.2024

| | | | | | | |
|----|-----------------------------------|--------------|--|-------------------------------|--------------|---|
| 01 | Sector | | Local Authority Road | | | |
| 02 | Location | | Jaffna | | | |
| 03 | Source of fund | | PSDG | | 05 | |
| 04 | Name of the Activity | | Reconstruction of Varuthalaivilan Housing scheme Road Valigamam north PS | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 10.07.2024 | | | |
| 10 | Date of Completion | | 05.09.2024 | | | |
| 11 | Imprest Confirmed date | | | | | |
| 12 | TEC (Mn) | | 5.000 | | | |
| 13 | Contract Amount | | 3.157 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 5.000 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed.and Final Payment Recommended Rs.1,085,831.88 | | | |



Last Updated - 11.10.2024

| | | | | | | |
|----|-----------------------------------|--------------|---|-------------------------------|--------------|--|
| 01 | Sector | | Local Authority Road | | | |
| 02 | Location | | Jaffna | | | |
| 03 | Source of fund | | PSDG | | 08 | |
| 04 | Name of the Activity | | Reconstruction of Moonram Panai Vairavar Kovil Road, Vaddukodai - Valikamam West PS | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 18.07.2024 | | | |
| 10 | Date of Completion | | 13.10.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 2.740 | | | |
| 13 | Contract Amount | | | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 2.740 | Expenditure (Rs in Mn) | 2024 | |
| | | Total | | | Total | |
| 16 | Remarks | | Work Completed. Final Payment Recommended Rs1053365.72 | | | |



Last Updated - 13.10.2024

| | | | | | | |
|----|-----------------------------------|--------------|--|-------------------------------|--------------|---|
| 01 | Sector | | Local Authority Road | | | |
| 02 | Location | | Jaffna | | | |
| 03 | Source of fund | | PSDG | | 09 | |
| 04 | Name of the Activity | | Renovation of Periyapulam 2nd lane at Naranthanai - Kayts PS | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 05.07.2024 | | | |
| 10 | Date of Completion | | 05.09.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 5.000 | | | |
| 13 | Contract Amount | | 2.994 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 2.994 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed. Final Payment recommended Rs 2,980,31.94 | | | |




Last Updated - 05.09.2024

| | | | | | | |
|----|-----------------------------------|--------------|---|-------------------------------|--------------|--|
| 01 | Sector | | Local Authority Road | | | |
| 02 | Location | | Jaffna | | | |
| 03 | Source of fund | | PSDG | | 10 | |
| 04 | Name of the Activity | | Reconstruction of Maligai Servarkar Kovil Veethy ,Karainagar -Karainagar PS | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 27.06.2024 | | | |
| 10 | Date of Completion | | 30.08.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 5.000 | | | |
| 13 | Contract Amount | | 3.710 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 5.000 | Expenditure (Rs in Mn) | 2024 | |
| | | Total | | | Total | |
| 16 | Remarks | | Work completed. Final Payment recommended Rs 379,261.10 | | | |



Last Updated - 31.10.2024

| | | | | | | |
|----|-----------------------------------|--------------|--|-------------------------------|--------------|---|
| 01 | Sector | | Local Authority Road | | | |
| 02 | Location | | Jaffna | | | |
| 03 | Source of fund | | PSDG | | 11 | |
| 04 | Name of the Activity | | Construction of Kalikovil Road 14th Road - Chavakachchery PS | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 31.07.2024 | | | |
| 10 | Date of Completion | | 22.10.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 5.000 | | | |
| 13 | Contract Amount | | 4.985 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 4.985 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | |
| 16 | Remarks | | Work Completed. Final Payment Recommended Rs. 2,701,956.32 | | | |

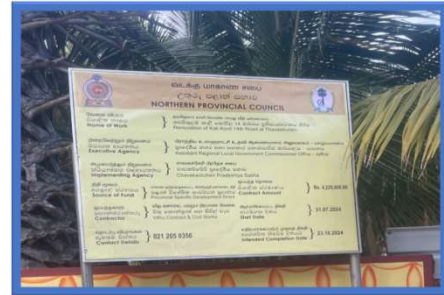

Last Updated 30.11.2024

| | | | | | | |
|----|-----------------------------------|--------------|---|-------------------------------|--------------|--|
| 01 | Sector | | Local Authority Road | | | |
| 02 | Location | | Kilinochchi | | | |
| 03 | Source of fund | | PSDG | | 17 | |
| 04 | Name of the Activity | | Reconstruction of Sepasthiyarpuram Road, Mulankavil -Poonakary Pradeshiya Sabha | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 01.07.2024 | | | |
| 10 | Date of Completion | | 22.09.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 6.000 | | | |
| 13 | Contract Amount | | 6.000 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 6.000 | Expenditure (Rs in Mn) | 2024 | |
| | | Total | | | Total | |
| 16 | Remarks | | Work Completed. Final Payment recommended Rs 3929642.60 | | | |



Last Updated - 08.10.2024

| | | | | | | |
|----|-----------------------------------|--------------|--|-------------------------------|--------------|---|
| 01 | Sector | | Local Authority Road | | | |
| 02 | Location | | Mullaitivu | | | |
| 03 | Source of fund | | PSDG | | 25 | |
| 04 | Name of the Activity | | Construction of Inthupuram main Road - stage - II - Puthukkudiyiruppu PS | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 02.06.2024 | | | |
| 10 | Date of Completion | | 12.09.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 3.000 | | | |
| 13 | Contract Amount | | 3.000 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 3.000 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed. Final Payment Recommended Rs. 519507.62 | | | |



Last up date 12.09.2024

| | | | | | | |
|----|-----------------------------------|--------------|---|-------------------------------|--------------|---|
| 01 | Sector | | Local Authority Road | | | |
| 02 | Location | | Mullaitivu | | | |
| 03 | Source of fund | | PSDG | | 27 | |
| 04 | Name of the Activity | | Construction of Thurka Road 1st Lane, Kompavil - Puthukkudiyiruppu PS | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 02.06.2024 | | | |
| 10 | Date of Completion | | 15.08.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 4.000 | | | |
| 13 | Contract Amount | | 4.000 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 4.000 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed. Final payment recommended Rs. 3291180.62 | | | |



Last up date 10.10.2024

| 01 | Sector | Local Authority Road | | | | |
|----|----------------------------|---|-------|------------------------|-------|-------|
| 02 | Location | Nedunkerny Maraviluppai Road at Vavuniya | | | | |
| 03 | Source of fund | PSDG | | | | |
| 04 | Name of the Activity | Construction of Mettaling & Taring at Nedunkerny Maraviluppai Road- Vavuniya North PS | | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | New | | | | |
| 07 | Type | Civil | | | | |
| 08 | Date of Approval | 20.03.2023 | | | | |
| 09 | Date of Commence | 10.12.2023 | | | | |
| 10 | Date of Completion | 17.02.2024 | | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | 6.00 | | | | |
| 13 | Contract Amount | | | | | |
| 14 | Physical Progress | 100% | | | | |
| 15 | Allocation (Rs in Mn) | 2023 | 6.00 | Expenditure (Rs in Mn) | 2023 | 4.732 |
| | | 2024 Continue | 1.267 | | 2024 | |
| | | Total | | | Total | - |
| 16 | Remarks | Work Completed.Final payment Recommended ,Rs.1240760.86 | | | | |



Last Updated - 29.02.2024

| 01 | Sector | Local Authority Road | | | | |
|----|----------------------------|---|-------|------------------------|-------|---|
| 02 | Location | Vavuniya | | | | |
| 03 | Source of fund | PSDG | 33 | | | |
| 04 | Name of the Activity | Reconstruction of metarling and taringat Mannar Road 8 th Lane, Marakkarambai - Vavuniya South | | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | New | | | | |
| 07 | Type | Civil | | | | |
| 08 | Date of Approval | 06.03.2024 | | | | |
| 09 | Date of Commence | 05.06.2024 | | | | |
| 10 | Date of Completion | 12.09.2024 | | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | 10.670 | | | | |
| 13 | Contract Amount | 10.670 | | | | |
| 14 | Physical Progress | 100% | | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 8.845 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | Work Completed. Final Payment recommended Rs. 4240023.90 | | | | |



Last Updated - 12.10.2024

| 01 | Sector | | Local Authority Road | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 02 | Location | | Vavuniya | | | |
| 03 | Source of fund | | PSDG | | 34 | |
| 04 | Name of the Activity | | Construction of Mannar Road 8th Lane, - Vavuniya (Stage - 02) | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 31.08.2024 | | | |
| 10 | Date of Completion | | 01.11.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 1.824 | | | |
| 13 | Contract Amount | | 1.824 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 1.824 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed. Final Payment recommended Rs 1805668.03 | | | |



Last Updated - 09.11.2024

| 01 | Sector | | Local Authority Road | | | |
|----|----------------------------|-------|--|------------------------|-------|---|
| 02 | Location | | Vavuniya | | | |
| 03 | Source of fund | | PSDG | | 37 | |
| 04 | Name of the Activity | | Reconstruction of MPCs Road, Nedunkerny South - | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 06.06.2024 | | | |
| 10 | Date of Completion | | 10.09.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 10.00 | | | |
| 13 | Contract Amount | | 7.328 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 10.00 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed Final payment recommended Rs 1015002.96 | | | |



Last Updated - 10.09.2024

| 01 | Sector | | Community Water Supply | | | |
|----|----------------------------|-------|--|------------------------|-------|---|
| 02 | Location | | Jaffna | | | |
| 03 | Source of fund | | PSDG | | 01 | |
| 04 | Name of the Activity | | Extension Water supply at Senthankulam (Stage1)- Vali North PS | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 20.03.2023 | | | |
| 09 | Date of Commence | | 29.08.2023 | | | |
| 10 | Date of Completion | | 30.01.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 5.000 | | | |
| 13 | Contract Amount | | | | | |
| 14 | Physical Progress | | 100% | | | |
| | Allocation (Rs in Mn) | 2024 | 5.000 | Expenditure (Rs in Mn) | 2024 | |
| | | | | | | |
| | | Total | | | Total | - |
| 16 | Remarks | | Work completed. Final payment Recommended Rs. 129, 995.39 | | | |



Last Updated - 14.03.2024

| 01 | Sector | | Community Water Supply | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 02 | Location | | Velanai PS at Jaffna | | | |
| 03 | Source of fund | | PSDG | | 02 | |
| 04 | Name of the Activity | | Repairing of stainless water bowsers -03 Nos - Velanai PS | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 20.03.2023 | | | |
| 09 | Date of Commence | | 29.12.2023 | | | |
| 10 | Date of Completion | | 27.01.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 2.800 | | | |
| 13 | Contract Amount | | | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2023 | 2.800 | Expenditure (Rs in Mn) | 2023 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed. final payment Recommended Rs 2790000.00 | | | |



Last Updated -

| 01 | Sector | | Community Water Supply | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 02 | Location | | Kilinochchi | | | |
| 03 | Source of fund | | PSDG | | 06 | |
| 04 | Name of the Activity | | Drinking water supply system for the Kilinochchi service market- Karachchi PS | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 20.03.2023 | | | |
| 09 | Date of Commence | | 17.11.2023 | | | |
| 10 | Date of Completion | | 05.01.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 11 | TEC (Mn) | | 4.000 | | | |
| 12 | Contract Amount | | | | | |
| 13 | Physical Progress | | 100% | | | |
| 14 | Allocation (Rs in Mn) | 2024 | 4.000 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 15 | Remarks | | Work Completed. Final Payment recommended Rs. 2,772,329.81 | | | |



Last Updated -09.02.2024

| 01 | Sector | | Waste Management | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 02 | Location | | Jaffna | | | |
| 03 | Source of fund | | PSDG | | 01 | |
| 04 | Name of the Activity | | Extention of concrete Flat building for compost project at Waste Management Center at Kallundai- Vali South West PS | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Con | | | |
| 08 | Date of Approval | | 20.03.2023 | | | |
| 09 | Date of Commence | | 06.09.2023 | | | |
| 10 | Date of Completion | | 12.12.2023 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 4.969 | | | |
| 13 | Contract Amount | | | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 2.107 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 65 | Remarks | | Work completed. Final Payment Recommended Rs. 2110000.00 | | | |



Last Updated - 12.12.2023

| 01 | Sector | | Waste Management | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 02 | Location | | Kilinochchi | | | |
| 03 | Source of fund | | PSDG | | 06 | |
| 04 | Name of the Activity | | Balance work of Construction of Dumping Ground Access Road at Araththinagar in Pallai | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | Con | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 20.03.2023 | | | |
| 09 | Date of Commence | | 07.09.2023 | | | |
| 10 | Date of Completion | | 06.02.2024 | | | |
| 11 | Imprest Confirmed date | | | | | |
| 12 | TEC (Mn) | | 3.500 | | | |
| 13 | Contract Amount | | | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 0.942 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed.Final Payment recommended Rs . 879259.77 | | | |



Last Updated - 27.02.2024

| 01 | Sector | | Waste Management | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 02 | Location | | Mulaitivu | | | |
| 03 | Source of fund | | PSDG | | 09 | |
| 04 | Name of the Activity | | Improvement of Waste collecting Center at Mulliwaikkal - Maritimepattu PS | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | Con | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | | | | |
| 09 | Date of Commence | | 31.10.2023 | | | |
| 10 | Date of Completion | | 01.01.2024 | | | |
| 11 | Imprest Confirmed Date | | 12.03.2024 | | | |
| 12 | TEC (Mn) | | 2.000 | | | |
| 13 | Contract Amount | | | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 0.225 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work completed. Final Payment Recommended RS . 70459.19 | | | |



Last Updated 12.03.2024

| 01 | Sector | | Waste Management | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 02 | Location | | Mullaitivu | | | |
| 03 | Source of fund | | PSDG | | 10 | |
| 04 | Name of the Activity | | Construction of Compost Yard at Mannankandal, Puthukkudiyiruppu PS (Stage - II) | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | Con | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 20.03.2023 | | | |
| 09 | Date of Commence | | 18.12.2023 | | | |
| 10 | Date of Completion | | 14.01.2024 | | | |
| 11 | Imprest Confirmed date | | | | | |
| 12 | TEC (Mn) | | 1.636 | | | |
| 13 | Contract Amount | | | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 0.804 | Expenditure (Rs in Mn) | 2023 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work completed. Final Payment Recommended Rs. 537,201.17 | | | |



Last Updated - 06.03.2024

| 01 | Sector | | Local Authority Services | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 02 | Location | | Mullaitivu | | | |
| 03 | Source of fund | | PSDG | | 06 | |
| 04 | Name of the Activity | | Pandiyankulam Preschool tube well and Toilet Bathroom - Manthai East PS | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 20.03.2023 | | | |
| 09 | Date of Commence | | 08.11.2023 | | | |
| 10 | Date of Completion | | 05.02.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 2.000 | | | |
| 13 | Contract Amount | | | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 0.664 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work completed Final Payment recommended Rs 391462.93 | | | |



Last Updated - 30.04.2024

| | | | | | | |
|----|----------------------------|-------|--|------------------------|-------|---|
| 01 | Sector | | Local Authority Services | | | |
| 02 | Location | | Mullaitivu | | | |
| 03 | Source of fund | | PSDG | 07 | | |
| 04 | Name of the Activity | | Modification of Olumadu market Shopping unit -Puthukkudiyiruppu PS | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 20.06.2024 | | | |
| 10 | Date of Completion | | 06.09.2024 | | | |
| 11 | Imprest Confirmed date | | | | | |
| 12 | TEC (Mn) | | 3.000 | | | |
| 13 | Contract Amount | | 3.000 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 3.000 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | |
| 16 | Remarks | | Work Completed.Final Payment Recommended 3,000,000.00 | | | |



Last Updated - 06.09.2024

| | | | | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 01 | Sector | | Local Authority Services | | | |
| 02 | Location | | Mannar | | | |
| 03 | Source of fund | | PSDG | 16 | | |
| 04 | Name of the Activity | | Construction of Fencing at Sirukkandal Public Cemetary- Nanattan PS | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Con | | | |
| 08 | Date of Approval | | | | | |
| 09 | Date of Commence | | 27.09.2023 | | | |
| 10 | Date of Completion | | 13.12.2023 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 1.000 | | | |
| 13 | Contract Amount | | | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2023 | 0.389 | Expenditure (Rs in Mn) | 2023 | - |
| | | Total | | | Total | |
| 16 | Remarks | | Work Completed. Final payment recommended Rs. 310,920,91 | | | |



Last Updated 29.02.2024

| 01 | Sector | | Local Authority Services | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 02 | Location | | Mannar | | | |
| 03 | Source of fund | | PSDG | | 17 | |
| 04 | Name of the Activity | | Construction of Burning Center and Fencing at Iranai Illuppaikulam- Manthai West PS | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 20.03.2023 | | | |
| 09 | Date of Commence | | 11.09.2023 | | | |
| 10 | Date of Completion | | 13.01.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 2.000 | | | |
| 13 | Contract Amount | | | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 0.130 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed. Final Payment Recommended Rs 58586.01. | | | |



Last Updated - 29.02.2024

| 01 | Sector | | Local Authority Services | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 02 | Location | | Mannar | | | |
| 03 | Source of fund | | PSDG | | 18 | |
| 04 | Name of the Activity | | Construction of Chicken Meat Stall- Chilawaththurai- Musali P.S | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | | | | |
| 09 | Date of Commence | | 25.09.2023 | | | |
| 10 | Date of Completion | | 05.12.2023 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 11 | TEC (Mn) | | 2.000 | | | |
| 12 | Contract Amount | | | | | |
| 13 | Physical Progress | | 100% | | | |
| 14 | Allocation (Rs in Mn) | 2024 | 1.442 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 15 | Remarks | | Work Completed. Final Payment recommended Rs. 1,383,775.47 | | | |



Last Updated - 29.02.2024

| 01 | Sector | | Rural Development | | | |
|----|----------------------------|-------|--|------------------------|-------|---|
| 02 | Location | | Renovation of Puliyady Lane, Velanai | | | |
| 03 | Source of fund | | PSDG | 01 | | |
| 04 | Name of the Activity | | Renovation of Puliyady Lane, Velanai | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 22.04.2024 | | | |
| 10 | Date of Completion | | 14.06.2024 | | | |
| 11 | Imprest Confirmed date | | | | | |
| 12 | TEC (Mn) | | 1.20 | | | |
| 13 | Contract Amount | | 1.20 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 1.20 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed, Final Payment recommended Rs. 1,197,499.46 | | | |



Last Updated - 02.08.2024

| 01 | Sector | | Rural Development | | | |
|----|----------------------------|-------|--|------------------------|-------|---|
| 02 | Location | | Renovation works in Chunnagam South Kathiramalai Lane - Vali South, Jaffna | | | |
| 03 | Source of fund | | PSDG | 02 | | |
| 04 | Name of the Activity | | Renovation works in Chunnagam South Kathiramalai Lane - Vali South, Jaffna | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 16.04.2024 | | | |
| 10 | Date of Completion | | 14.06.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 1.000 | | | |
| 13 | Contract Amount | | | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 1.000 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed. Final Payment Recommended Rs 942,965.50 | | | |



Last Updated - 11.12.2024

| 01 | Sector | | Rural Development | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 02 | Location | | Construction of Barathy Lane Irupalai South - Vali East | | | |
| 03 | Source of fund | | PSDG | 03 | | |
| 04 | Name of the Activity | | Construction of Barathy Lane Irupalai South - Vali East | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 09.05.2024 | | | |
| 10 | Date of Completion | | 14.06.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 2.90 | | | |
| 13 | Contract Amount | | 2.90 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 2.90 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed. Final Payment Recommended Rs.2,764,745.40 | | | |





Last Updated - 30.07.2024

| 01 | Sector | | Rural Development | | | |
|----|----------------------------|-------|--|------------------------|-------|--|
| 02 | Location | | Mathagal West , Jaffna | | | |
| 03 | Source of fund | | PSDG | 04 | | |
| 04 | Name of the Activity | | Renovation Works in Mathagal West WRDS Building | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 16.04.2024 | | | |
| 10 | Date of Completion | | 24.07.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 0.900 | | | |
| 13 | Contract Amount | | | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 0.900 | Expenditure (Rs in Mn) | 2024 | |
| | | Total | | | Total | |
| 16 | Remarks | | Work Completed. Final payment recommended Rs 274432.29 | | | |





Last Updated - 05.09.2024

| 01 | Sector | | Rural Development | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 02 | Location | | Kilinochchi | | | |
| 03 | Source of fund | | PSDG | 06 | | |
| 04 | Name of the Activity | | Construction of 3rd cross road - Culvert, Uruthirapuram | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 27.06.2024 | | | |
| 10 | Date of Completion | | 20.08.2024 | | | |
| 11 | Imprest Confirmed date | | | | | |
| 12 | TEC (Mn) | | 1.500 | | | |
| 13 | Contract Amount | | 1.500 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 1.500 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed. Final payment recommended Rs.665267.88 | | | |

Last Updated -20.11.2024

| 01 | Sector | | Rural Development | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 02 | Location | | Kilinochchi | | | |
| 03 | Source of fund | | PSDG | 07 | | |
| 04 | Name of the Activity | | Construction of 1st cross road - Culvert, Uruthirapuram | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 27.06.2024 | | | |
| 10 | Date of Completion | | 17.08.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 1.500 | | | |
| 13 | Contract Amount | | 1.500 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 1.500 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed. Final payment recommended Rs 665,334.36 | | | |

Last Updated - 21.11.2024

| 01 | Sector | | Rural Development | | | |
|----|----------------------------|-------|--|------------------------|-------|---|
| 02 | Location | | Kilinochchi | | | |
| 03 | Source of fund | | PSDG | | 08 | |
| 04 | Name of the Activity | | Construction of Murasumoddai RDS Paddy Field Road with Culvert, Kandawalai | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 30.05.2024 | | | |
| 10 | Date of Completion | | 25.06.2024 | | | |
| 11 | Imprest Confirmed date | | | | | |
| 12 | TEC (Mn) | | 4.000 | | | |
| 13 | Contract Amount | | 4.000 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 4.000 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | work Completed. Final payment recommended Rs 333155.00 | | | |



Last Updated - 05.12.2024

| 01 | Sector | | Rural Development | | | |
|----|----------------------------|-------|--|------------------------|-------|---|
| 02 | Location | | Renovation of 9 th Cross Road at Mangaikudiyituppu Thunukkai , Mullaitivu | | | |
| 03 | Source of fund | | PSDG | | 09 | |
| 04 | Name of the Activity | | Renovation of 9 th Cross Road at Mangaikudiyituppu Thunukkai | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 18.04.2024 | | | |
| 10 | Date of Completion | | 28.06.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 2.00 | | | |
| 13 | Contract Amount | | | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 2.00 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed, Final Payment recommended Rs.1,973,398.52 | | | |



Last Updated - 01.08.2024

| 01 | Sector | Rural Development | | | |
|----|----------------------------|--|-------|------------------------|------|
| 02 | Location | Unnapilavu , Maritimpeattu | | | |
| 03 | Source of fund | PSDG | 10 | | |
| 04 | Name of the Activity | Renovation of Connecting Road from DS Office to Mullaitivu Mankulam Road with Culverts at Unnapilavu , Maritimpeattu | | | |
| 05 | Activity No | | | | |
| 06 | Stats of The Project (N/C) | New | | | |
| 07 | Type | Civil | | | |
| 08 | Date of Approval | 06.03.2024 | | | |
| 09 | Date of Commence | 13.04.2024 | | | |
| 10 | Date of Completion | 17.07.2024 | | | |
| 11 | Imprest Confirmed date | | | | |
| 12 | TEC (Mn) | 5.000 | | | |
| 13 | Contract Amount | | | | |
| 14 | Physical Progress | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 5.000 | Expenditure (Rs in Mn) | 2024 |
| | | Total | | Total | |
| 16 | Remarks | Work Completed .Final Payment recommended Rs.3953900.82 | | | |



Last Updated - 03.09.2024

| 01 | Sector | Rural Development | | | |
|----|----------------------------|---|-------|------------------------|------|
| 02 | Location | Vavuniya | | | |
| 03 | Source of fund | PSDG | 12 | | |
| 04 | Name of the Activity | Renovation of Makilankulam (120 Meeter) Internal road& 01 Culvert, Vavuniya | | | |
| 05 | Activity No | | | | |
| 06 | Stats of The Project (N/C) | New | | | |
| 07 | Type | Civil | | | |
| 08 | Date of Approval | 06.03.2024 | | | |
| 09 | Date of Commence | 02.05.2024 | | | |
| 10 | Date of Completion | 29.05.2024 | | | |
| 11 | Imprest Confirmed date | | | | |
| 12 | TEC (Mn) | 2.000 | | | |
| 13 | Contract Amount | | | | |
| 14 | Physical Progress | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 2.000 | Expenditure (Rs in Mn) | 2024 |
| | | Total | | Total | - |
| 16 | Remarks | Work Completed. Final Payment Recommended Rs. 2,000,000.00 | | | |



Last Updated

| 01 | Sector | | Rural Development | | | |
|----|----------------------------|-------|---|------------------------|-------|--|
| 02 | Location | | Mamadu, VavuniyaNorth | | | |
| 03 | Source of fund | | PSDG | 13 | | |
| 04 | Name of the Activity | | Renovation of Mamadu115M InternalRoad (Congrete Road) VavuniyaNorth | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 06.05.2024 | | | |
| 10 | Date of Completion | | 30.07.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 2.000 | | | |
| 13 | Contract Amount | | | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 2.000 | Expenditure (Rs in Mn) | 2024 | |
| | | Total | | | Total | |
| 16 | Remarks | | Work completed. Final payment recommended Rs. 2,000,000.00 | | | |



Last Updated - 06.09.2024

| 01 | Sector | | Rural Development | | | |
|----|----------------------------|-------|--|------------------------|-------|---|
| 02 | Location | | Renovation of palayawade(2KM) internal Road&01Culvert,Vavuniya North | | | |
| 03 | Source of fund | | PSDG | 14 | | |
| 04 | Name of the Activity | | Renovation of palayawade(2KM) internal Road&01Culvert,Vavuniya North | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 18.04.2024 | | | |
| 10 | Date of Completion | | 29.05.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 2.500 | | | |
| 13 | Contract Amount | | | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 2.500 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed. Final Payment Recommended Rs. 2,500,000.00 | | | |



Last Updated - 02.06.2024

| 01 | Sector | Rural Development | | | |
|----|----------------------------|---|-------|------------------------|------|
| 02 | Location | Senaipilavu, Vavuniya North | | | |
| 03 | Source of fund | PSDG | 15 | | |
| 04 | Name of the Activity | Renovation of senaipilavu(1KM) internal Road&02Culvert,Vavuniya North | | | |
| 05 | Activity No | | | | |
| 06 | Stats of The Project (N/C) | New | | | |
| 07 | Type | Civil | | | |
| 08 | Date of Approval | 06.03.2024 | | | |
| 09 | Date of Commence | 18.04.2024 | | | |
| 10 | Date of Completion | 30.07.2024 | | | |
| 11 | Imprest Confirmed Date | | | | |
| 12 | TEC (Mn) | 1.500 | | | |
| 13 | Contract Amount | | | | |
| 14 | Physical Progress | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 1.500 | Expenditure (Rs in Mn) | 2024 |
| | | Total | | Total | |
| 16 | Remarks | Work Completed.Final Payment Recommended Rs 1,500,000.00 | | | |



Last Updated - 06.09.2024

| 01 | Sector | Rural Development | | | |
|----|----------------------------|---|------|------------------------|------|
| 02 | Location | Construction of Cremation shet & Gate with Boundery Wall at Veerapuram Cemetery, Cheddikkulam | | | |
| 03 | Source of fund | PSDG | 16 | | |
| 04 | Name of the Activity | Costruction of Cremation shet & Gate with Boundery Wall at Veerapuram Cemetery, Cheddikkulam | | | |
| 05 | Activity No | | | | |
| 06 | Stats of The Project (N/C) | New | | | |
| 07 | Type | Civil | | | |
| 08 | Date of Approval | 06.03.2024 | | | |
| 09 | Date of Commence | 30.04.2024 | | | |
| 10 | Date of Completion | 10.06.2024 | | | |
| 12 | TEC (Mn) | 2.0 | | | |
| 13 | Contract Amount | 2.0 | | | |
| 14 | Physical Progress | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 2.00 | Expenditure (Rs in Mn) | 2024 |
| | | Total | | Total | - |
| 16 | Remarks | Work completed. Final Payment recommended Rs 1968451.59 | | | |



Last Updated - 28.06.2024

| 01 | Sector | | Rural Development | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 02 | Location | | Arasadikkulam, Vavuniya | | | |
| 03 | Source of fund | | PSDG | 17 | | |
| 04 | Name of the Activity | | Construction of Cremation Shet Arasadikkulam & Open dug well Arasadikkulam, Chedikkulam | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 30.04.2024 | | | |
| 10 | Date of Completion | | 10.06.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 2.0 | | | |
| 13 | Contract Amount | | 2.0 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 2.0 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work completed. Final Payment recommended Rs 1947251.33 | | | |



Last Update 28.06.2024

| 01 | Sector | | Rural Development | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 02 | Location | | Vavuniya | | | |
| 03 | Source of fund | | PSDG | 18 | | |
| 04 | Name of the Activity | | Renovation of Iyankaravoor Internal road(2Km) ,Vavuniya | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 11.09.2024 | | | |
| 10 | Date of Completion | | 06.12.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 2.500 | | | |
| 13 | Contract Amount | | | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 2.500 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed. Final Payment recommended Rs 147,000.00 | | | |



Last updated 06.12.2024

| 01 | Sector | | Rural Development | | | |
|----|----------------------------|-------|--|------------------------|-------|---|
| 02 | Location | | Vavuniya | | | |
| 03 | Source of fund | | PSDG | 19 | | |
| 04 | Name of the Activity | | Construction of 7 Culvert at Muthirampiddy, Vavuniya North | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 09.09.2024 | | | |
| 10 | Date of Completion | | 05.11.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 1.500 | | | |
| 13 | Contract Amount | | 1.500 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 1.500 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work completed. Final Payment recommended Rs 1,500,000.00 | | | |



Last Updated 28.11.2024

| 01 | Sector | | Rural Development | | | |
|----|----------------------------|-------|--|------------------------|-------|---|
| 02 | Location | | Mannar | | | |
| 03 | Source of fund | | PSDG | 20 | | |
| 04 | Name of the Activity | | Construction of Calvert and Renovation of Road at Kayakuli Cemetery Road | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 19.06.2024 | | | |
| 10 | Date of Completion | | 30.09.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 1.900 | | | |
| 13 | Contract Amount | | 1.900 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 1.900 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed. Final Payment Recommended. Rs.1,411,422.94 | | | |



Last Updated - 01.10.2024

| 01 | Sector | | Rural Development | | | |
|----|----------------------------|-------|---|------------------------|-------|--|
| 02 | Location | | Mannar | | | |
| 03 | Source of fund | | PSDG | 21 | | |
| 04 | Name of the Activity | | Renovation of Internal Concret Road at 5th Cross Street. Rathapur, Vankalai | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 02.05.2024 | | | |
| 10 | Date of Completion | | 01.08.2024 | | | |
| 11 | Imprest Confirmed date | | | | | |
| 12 | TEC (Mn) | | 2.500 | | | |
| 13 | Contract Amount | | 2.500 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 2.500 | Expenditure (Rs in Mn) | 2024 | |
| | | Total | | | Total | |
| 16 | Remarks | | Work completed. Final Payment Recommended Rs.2,498,229.87 | | | |



Last Updated - 01.08.2024

| 01 | Sector | | Rural Development | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 02 | Location | | Mannar | | | |
| 03 | Source of fund | | PSDG | 22 | | |
| 04 | Name of the Activity | | Construction of Calvert and Earth Filling at Vellimalai, Musali | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 19.06.2024 | | | |
| 10 | Date of Completion | | 11.10.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 0.600 | | | |
| 13 | Contract Amount | | 0.600 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 0.600 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work completed. Final Payment recommended Rs. 592665.53 | | | |



Last Updated - 11.10.2024



| 01 | Sector | Rural Development | | | | |
|----|----------------------------|--|-------|------------------------|-------|----|
| 02 | Location | Mannar | | | | |
| 03 | Source of fund | PSDG | | | | 23 |
| 04 | Name of the Activity | Renovation of 100 M Internal Concret Road with Calvert at Karungkalimodai ,Palaperumalkadhu. | | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | New | | | | |
| 07 | Type | Civil | | | | |
| 08 | Date of Approval | 06.03.2024 | | | | |
| 09 | Date of Commence | 30.04.2024 | | | | |
| 10 | Date of Completion | 30.08.2024 | | | | |
| 11 | Imprest Confirmed date | | | | | |
| 12 | TEC (Mn) | 3.500 | | | | |
| 13 | Contract Amount | 3.500 | | | | |
| 14 | Physical Progress | 100% | | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 3.500 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | Work completed. Final Payment recommended. Rs 3366114.59 | | | | |






Last Updated 23.10.2024

| 01 | Sector | Rural Development | | | | |
|----|----------------------------|--|-------|------------------------|-------|----|
| 02 | Location | Partial Renovation of WRDS Building at Pesalai North- Mannar | | | | |
| 03 | Source of fund | PSDG | | | | 25 |
| 04 | Name of the Activity | Partial Renovation of WRDS Building at Pesalai North- Mannar | | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | New | | | | |
| 07 | Type | Civil | | | | |
| 08 | Date of Approval | 06.03.2024 | | | | |
| 09 | Date of Commence | 06.05.2024 | | | | |
| 10 | Date of Completion | 04.07.2024 | | | | |
| 11 | Imprest confirmed Date | | | | | |
| 12 | TEC (Mn) | 0.400 | | | | |
| 13 | Contract Amount | 0.400 | | | | |
| 14 | Physical Progress | 100% | | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 0.400 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | Work Completed. Final Payment Recommended Rs 397,339.94 | | | | |



Last Updated - 16.07.2024

| 01 | Sector | | Road Development | | | |
|----|----------------------------|-------|--|-------|-------|---|
| 02 | Location | | Improvements of Punguduthivu Amman Kovil Road (0.950 - 1.625)km Jaffna | | | |
| 03 | Source of fund | | PSDG | 01 | | |
| 04 | Name of the Activity | | Improvements of Punguduthivu Amman Kovil Road (0.950 - 1.625)km | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 08.05.2024 | | | |
| 10 | Date of Completion | | 18.07.2024 | | | |
| 11 | Imprest Confirmed date | | | | | |
| 12 | TEC (Mn) | | 15.00 | | | |
| 13 | Contract Amount | | 10.09 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | Expenditure (Rs in Mn) | 2024 | - | |
| | | Total | | 10.09 | Total | - |
| 16 | Remarks | | Work Completed. Final payment Recommended Rs.2,386,234.26 | | | |





Last Updated - 19.07.2024

| 01 | Sector | | Road Development | | | |
|----|----------------------------|-------|---|-------|-------|--|
| 02 | Location | | Jaffna | | | |
| 03 | Source of fund | | PSDG | 02 | | |
| 04 | Name of the Activity | | Improvements of Punguduthivu Amman Kovil Road (1.625-2.625)km | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 07.08.2024 | | | |
| 10 | Date of Completion | | 28.09.2024 | | | |
| 11 | Imprest Confirmed date | | | | | |
| 12 | TEC (Mn) | | 4.000 | | | |
| 13 | Contract Amount | | 4.000 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | Expenditure (Rs in Mn) | 2024 | | |
| | | Total | | 4.000 | Total | |
| 16 | Remarks | | Work Completed. Final payment Recommended Rs,1,477,397.64 | | | |



Last Updated - 30.09.2024

| 01 | Sector | Road Development | | | | |
|----|----------------------------|--|--------|------------------------|-------|----|
| 02 | Location | Jaffna | | | | |
| 03 | Source of fund | PSDG | | | | 04 |
| 04 | Name of the Activity | Improvements to Analaitivu Central Road (0.000 – 1.750Km) | | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | New | | | | |
| 07 | Type | Civil | | | | |
| 08 | Date of Approval | 18.03.2024 | | | | |
| 09 | Date of Commence | 09.05.2024 | | | | |
| 10 | Date of Completion | 19.09.2024 | | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | 25.000 | | | | |
| 13 | Contract Amount | 24.270 | | | | |
| 14 | Physical Progress | 100% | | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 24.270 | Expenditure (Rs in Mn) | 2024 | |
| | | Total | | Total | Total | |
| 16 | Remarks | Work Completed. Final payment Recommended Rs. 6,130,000.00 | | | | |

Last Updated 30.09.2024

| 01 | Sector | Road Development | | | | |
|----|----------------------------|---|------|------------------------|-------|----|
| 02 | Location | Improvements of Kaddudai Navaly Road.(1.040 - 1.890) Km | | | | |
| 03 | Source of fund | PSDG | | | | 06 |
| 04 | Name of the Activity | Improvements of Kaddudai Navaly Road.(1.040 - 1.890) Km | | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | New | | | | |
| 07 | Type | Civil | | | | |
| 08 | Date of Approval | 06.03.2024 | | | | |
| 09 | Date of Commence | 08.05.2024 | | | | |
| 10 | Date of Completion | 18.07.2024 | | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | 9.40 | | | | |
| 13 | Contract Amount | 5.89 | | | | |
| 14 | Physical Progress | 100% | | | | |
| 15 | Allocation (Rs in Mn) | 2024 | | Expenditure (Rs in Mn) | 2024 | |
| | | Total | 6.96 | Total | Total | |
| 16 | Remarks | Work Completed. Final Payment Recommended Rs 2,470,845.07 | | | | |




Last Updated - 19.07.2024

| 01 | Sector | | Road Development | | | |
|----|----------------------------|-------|--|------------------------|-------|---|
| 02 | Location | | Jaffna | | | |
| 03 | Source of fund | | PSDG | 07 | | |
| 04 | Name of the Activity | | Improvements to Mandaitivu Loop Road (1.250 – 1.450 Km) | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 10.06.2024 | | | |
| 10 | Date of Completion | | 27.09.2024 | | | |
| 11 | Imprest Confirmed date | | | | | |
| 12 | TEC (Mn) | | 13.770 | | | |
| 13 | Contract Amount | | 10.974 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 9.770 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed. Final Payment Recommended Rs 280,000.000 | | | |



Last Updated – 27.09.2024

| 01 | Sector | | Road Development | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 02 | Location | | Mullaitivu | | | |
| 03 | Source of fund | | PSDG | 16 | | |
| 04 | Name of the Activity | | Construction of structure Ahatugaswewa Janakapura Road 3rd Km | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 22.05.2024 | | | |
| 10 | Date of Completion | | 12.08.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 15.00 | | | |
| 13 | Contract Amount | | 15.00 | | | |
| 14 | Physical Progress | | | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 15.00 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed. Final payment recommended Rs 5445624.72 | | | |



Last Updated –15.10.2024

| 01 | Sector | | Road Development | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 02 | Location | | Mullaitivu | | | |
| 03 | Source of fund | | PSDG | 17 | | |
| 04 | Name of the Activity | | Improvement of Thunukkai Thenniyankulam Road (2.0 – 5.0 km) | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 16.08.2024 | | | |
| 10 | Date of Completion | | 30.09.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 5.9000 | | | |
| 13 | Contract Amount | | 5.9200 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 5.9000 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed. Final payment recommended Rs 808260.60 | | | |



Last Updated - 15.10.2024

| 01 | Sector | | Road Development | | | |
|----|----------------------------|-------|---|------------------------|-------|--|
| 02 | Location | | Vavuniya | | | |
| 03 | Source of fund | | PSDG | 19 | | |
| 04 | Name of the Activity | | Improvements to Mahilankulam Pallamadhu Road (2.21- 3.68km) | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 15.05.2024 | | | |
| 10 | Date of Completion | | 08.08.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 25.000 | | | |
| 13 | Contract Amount | | | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 22.250 | Expenditure (Rs in Mn) | 2024 | |
| | | Total | | | Total | |
| 16 | Remarks | | Work completed and Final payment Recommended Rs 703,302.81 | | | |



Last Updated 09.08.2024

| 01 | Sector | | Road Development | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 02 | Location | | Vavuniya | | | |
| 03 | Source of fund | | PSDG | 20 | | |
| 04 | Name of the Activity | | Improvements to Muthaliyarkulam Anaivilunthan Road (0.00- 0.83km) | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 15.05.2024 | | | |
| 10 | Date of Completion | | 22.08.2024 | | | |
| 11 | Imprest Confirmed date | | | | | |
| 12 | TEC (Mn) | | 25.000 | | | |
| 13 | Contract Amount | | | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 25.000 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work completed and Final payment recommended Rs. 2,769,791.87 | | | |



Last Updated - 22.08.2024

| 01 | Sector | | Road Development | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 02 | Location | | Vavuniya | | | |
| 03 | Source of fund | | PSDG | 21 | | |
| 04 | Name of the Activity | | Construction of Causeway on Iretperiyakulam Puthoor Road 4.7th km & 5.05 km | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 15.05.2024 | | | |
| 10 | Date of Completion | | 30.09.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 22.000 | | | |
| 13 | Contract Amount | | 17.652 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 18.930 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed. Final payment recommended Rs. 692058.46 | | | |



Last Updated 28.10.2024

| 01 | Sector | | Road Development | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 02 | Location | | Mannar | | | |
| 03 | Source of fund | | PSDG | 23 | | |
| 04 | Name of the Activity | | Improvements to Vankalai Sirunavatkulam Road (0.62 - 1.67 km) | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 11.05.2024 | | | |
| 10 | Date of Completion | | 11.09.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 25.000 | | | |
| 13 | Contract Amount | | | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 20.980 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed. Final Payment recommended Rs. 703302.81 | | | |




Last Updated 12.08.2024

| 01 | Sector | | Road Development | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 02 | Location | | Mannar | | | |
| 03 | Source of fund | | PSDG | 24 | | |
| 04 | Name of the Activity | | Improvements to Vankalai Sirunavatkulam Road (1.72-2.60 km) | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 10.09.2024 | | | |
| 10 | Date of Completion | | 22.10.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 20.100 | | | |
| 13 | Contract Amount | | 13.500 | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 20.980 | Expenditure (Rs in Mn) | 2024 | - |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed. Final Payment recommended Rs. 456601.12 | | | |



Last Updated 25.10.2024

| 01 | Sector | | Road Development | | | |
|----|----------------------------|-------|---|------------------------|-------|---|
| 02 | Location | | Mannar | | | |
| 03 | Source of fund | | PSDG | | 26 | |
| 04 | Name of the Activity | | Improvements to Vankalai Central Road (0.000-.0.755 km) | | | |
| 05 | Activity No | | | | | |
| 06 | Stats of The Project (N/C) | | New | | | |
| 07 | Type | | Civil | | | |
| 08 | Date of Approval | | 06.03.2024 | | | |
| 09 | Date of Commence | | 24.06.2024 | | | |
| 10 | Date of Completion | | 23.09.2024 | | | |
| 11 | Imprest Confirmed Date | | | | | |
| 12 | TEC (Mn) | | 15.100 | | | |
| 13 | Contract Amount | | | | | |
| 14 | Physical Progress | | 100% | | | |
| 15 | Allocation (Rs in Mn) | 2024 | 15.100 | Expenditure (Rs in Mn) | 2024 | |
| | | Total | | | Total | - |
| 16 | Remarks | | Work Completed ,and Final Payment recommended Rs. 1,937191.58 | | | |

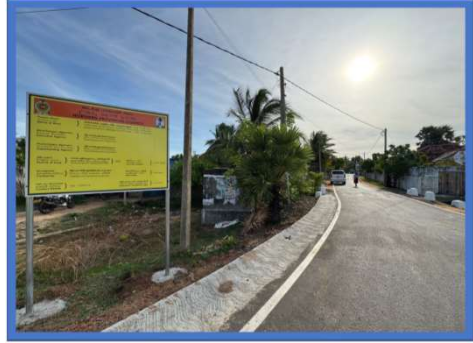

Last update 12.08.2024
