



IRRIGATION DEPARTMENT-NORTHERN PROVINCE



SECTORAL REVIEW MEETING

03.06.2025

OUT LINE OF PRESENTATION

- 1. INTRODUCTION TO SECTOR**
- 2. PROGRESS – GOSL FUND WORKS**
- 3. PROGRESS – FOREIGN FUNDED PROJECTS**
- 4. ISSUES**

1.2 LIVESTOCK PROGRESS 03.06.2025

ROLE OF NORTHERN PROVINCIAL COUNCIL IN WATER SECTOR

PROVISION IN THE CONSTITUTION

The Thirteenth Amendment to the Constitution in 1989

NINTH SCHEDULE OF THE CONSTITUTION

LIST - I (PROVINCIAL COUNCIL LIST)

19. Irrigation :

Planning, designing, implementation, supervision and maintenance of all irrigation works, other than Irrigation schemes relating to rivers running through more than one Province or inter provincial irrigation and land development schemes

1.2 LIVESTOCK PROGRESS 03.06.2025

OVERVIEW OF IRRIGATION STATUTE

LIST - III (CONCURRENT LIST)

17. Irrigation :

17.1 Water storage and management, drainage and embankments, flood protection, planning of water recourses;

17.2 Services provided for inter-provincial land and irrigation schemes, such as these relating to rural development, health, education, vocational training, co-operatives and other facilities.

1.2 LIVESTOCK PROGRESS 03.06.2025

NORTHERN PROVINCIAL IRRIGATION DEPARTMENT

MISSION

- Providing sustainable irrigation, flood control, drainage and salt water exclusion facilities by managing the schemes in Provincial River basins

VISION

- Self-sufficiency in food by developing a viable farming community through building up of irrigation schemes / Projects.

1.2 LIVESTOCK PROGRESS 03.06.2025

OTHER VITAL STATISTICS

Lagoon Schemes

Name	Total Acreage
Vadamarachy Lagoon	20000
Upparu Lagoon	11000

1.2 LIVESTOCK PROGRESS 03.06.2025

Major/Medium Schemes


District	No of schemes	Total Acreage
Vavuniya	18	5897
Mannar	7	4721
Kilinochchi	9	32550
Mullaitivu	20	25765
	54	68,933

Drainage Scheme

Name	Total Acreage
Valukkai Aru	2000

Salt Water Exclusion Schemes

District	No of schemes	Total Acreage
Jaffna	34	7561

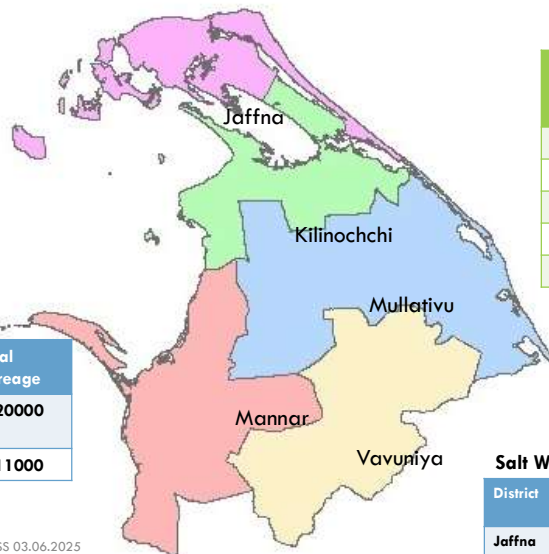

MAJOR SCHEMES

No	Name of Scheme	District	Irrigable Total in Acs. Area	Capacity in Ac.ft	Catch. Area in Sq.mls	No of Beneficiaries
1	Vavunikulam	Mullaitivu	6,897	35,300	88.00	3,020
2	Kanukkerny	Mullaitivu	1,813	2,100	26.25	120
3	Muthu Iyan Kaddu	Mullaitivu	6,112	41,000	65.75	3,110
4	Thanimurippu Kulam	Mullaitivu	2,364	15,000	51.00	828
5	Udayarkaddu Kulam	Mullaitivu	1,280	10,820	23.75	606
6	Akkarayan Kulam	Kilinochchi	3,417	21,200	41.20	1,819
7	Iranamadu	Kilinochchi	21,985	119,000	227.00	9,118
8	Kalmadu	Kilinochchi	3,450	9,152	26.50	750
9	Kariyalai Nagapaduwan	Kilinochchi	1,505	11,791	46.00	502
TOTAL			48,823	265,363	595.45	19,873

1.2 LIVESTOCK PROGRESS 03.06.2015

MEDIUM SCHEMES

Mullaitivu District

No	Name of Scheme	Irrigable Area Total in Acs.	Capacity in Ac.ft	Catch. Area in Sq.mls	No of Beneficiaries
1	Ampalaperumal	623	3,062	23.57	130
2	Iyan Kulam	952	3,950	13.50	376
3	Kalvilan Kulam	400	1,513	5.75	1,150
4	Koddaikaddiya Kulam	405	1,040	9.50	120
5	Kollavilan Kulam	262	787	2.40	143
6	Mallavi Kulam	325	740	1.85	70
7	Maruthan Kulam	450	1,700	10.30	104
8	Murukandy Kulam	356	1,780	7.55	150
9	Panankamam Kulam	300	725	1.50	75
10	Tenniyan Kulam	850	4,375	17.50	340
11	Therankandal Kulam	300	732	4.75	50
12	Madawalasingam	398	4,020	20.00	132
13	Neethukai Kulam	370	1,944	9.50	50
14	Visvamadu Kulam	808	3,020	12.80	415
15	Maruthamadu	500	3,600	-	128
Mullaitivu Total		7299	32,988	140.47	3,433

MEDIUM SCHEMES**Kilinochchi District**

No	Name of Scheme	Irrigable Area Total in Acs.	Capacity in Ac.ft	Catch. Area in Sq.mls	No of Beneficiaries
16	Kanagampigai	260	1,221	10.30	130
17	Piramanthal Aru	602	3,128	25.89	201
18	Puthumurippu	985	2,957	10.50	328
19	Vanneri	346	1,713	5.00	115
20	Kudamurutty Tank	680	2,950	-	640
	Kilinochchi Total	2,873	11,969	51.69	1,414

1.2 LIVESTOCK PROGRESS 03.06.2025

MEDIUM SCHEMES**Vavuniya District**

No	Name of Scheme	Irrigable Area Total in Acs.	Capacity in Ac.ft	Catch. Area in Sq.mls	No of Beneficiaries
21	Aliyamaruthamadu Tank	228	454	3.20	40
22	Chemamadu Tank	600	2560	14.50	200
23	Kalmadu Tank	400	1037	20.20	107
24	Kanagarayan Kulam	314	1100	3.50	210
25	Kombuvaitthakulam	210	524	2.40	40
26	Mallikai Kulam	300	815	2.45	68
27	Maharambai Kulam	215	650	6.10	50
28	Moonayamadu Kulam	215	324	21.70	50
29	Nampan Kulam	256	832	2.35	50
30	Pampaimadu	260	875	7.00	50
31	Vavuniya Tank	427	1970	10.50	104
32	Velan Kulam	224	735	1.90	35
33	Eropothana Tank	238	650	9.75	75
34	Madukanda Tank	400	1400	4.30	113
35	Nanchadichapallam Anicut	316	-	-	57
36	Mahakachchikodiya	257	970	7.20	210
37	Mamaduwa	659	3030	26.00	310
38	Periyathampanai	342	1095	9.12	114
	Vavuniya Total	5897	19,021	152.17	1,826

1.2 LIVESTOCK PROGRESS 03.06.2025

MEDIUM SCHEMES

Mannar District

No	Name of Scheme	Irrigable Area Total in Acs.	Capacity in Ac.ft	Catch. Area in Sq.mls	No of Beneficiaries
39	Admpan Kulam	400	580	4.50	130
40	Kurai Tank	750	2062	9.60	250
41	Periyamadu Tank	750	5780	142.00	250
42	Periyapandivirichchan	606	2816	32.40	202
43	Thadchanamaruthamad	530	1141	43.00	175
44	Welimaruthamadu	750	2766	156.00	250
45	Mullikulam	375	1500	12.67	125
Mannar Total		4,721	17,055	402.84	1,532

1.2 LIVESTOCK PROGRESS 03.06.2025

INTER PROVINCIAL SCHEMES-NATIONAL

Major/Medium Schemes

District	No of Schemes	Total Acreage
District	No of Schemes	Acreage
Vavuniya	6	13,550
Mannar	3	34,451


1.2 LIVESTOCK PROGRESS 03.06.2025

INTER PROVINCIAL SCHEMES - NATIONAL

Major/Medium Schemes

S.No	Name of Scheme	District	Major / Medium	Capacity	Full Supply Depth (FSD)	Command Area
1	Pavatkulam	Vavuniya	Major	27,000	19.33	4,134
2	Muhathankulam	Vavuniya	Medium	2,400	11.00	805
3	Maruthamadu	Vavuniya	Medium	1,500	12.00	438
4	Irratperiyakulam	Vavuniya	Medium	3,534	15.33	503
5	Rajendrankulam	Vavuniya	Medium	850	12.50	295
6	Kalaru Anicut	Vavuniya	Medium	-	3.25	600
7	Giant Tank	Mannar	Major	31,500	10.00	27,000
8	Akaththimurippu	Mannar	Major	8588	10.70	4537
9	Viyadikulam	Mannar	Major	1760	10.25	2914


ORGANIZATION

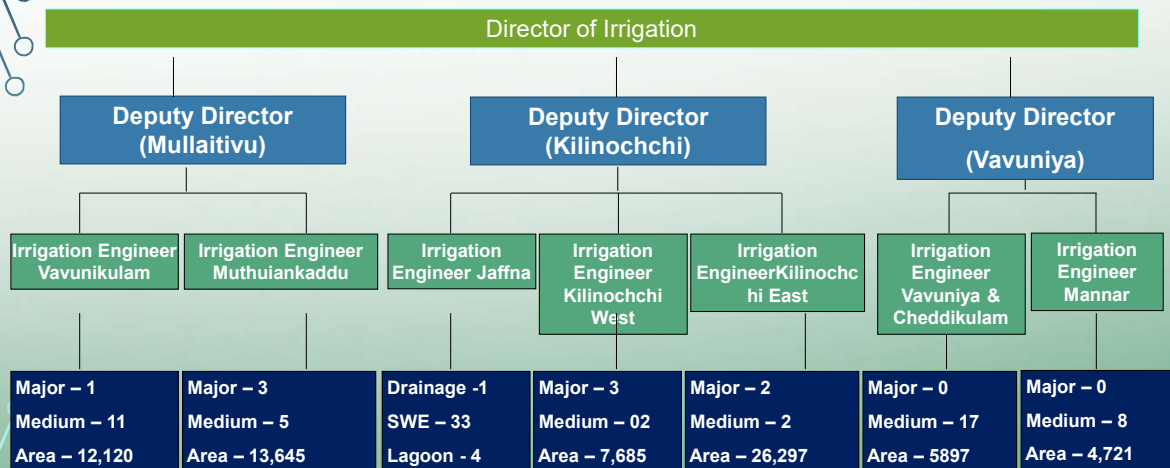

1.2 LIVESTOCK PROGRESS 03.06.2025

OVERVIEW – WATER RESOURCES IN SRILANKA

Historically Sri Lanka had great hydraulic Civilization

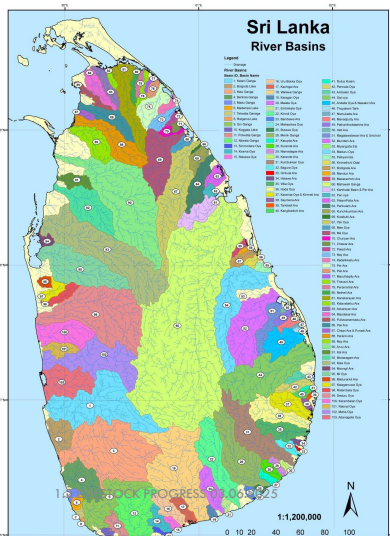


- 103 River Basins (*ganga droniya*)

Varying from 10 sq.km to over 10,000 sq.km

- More than 20 Wetlands
- Major /Medium /Minor Schemes
- Ground Water Sources
- Coastal and Marine Resources

OVERVIEW – WATER IN NORTHERN PROVINCE

We have fortunate “God Gifted” Water Resource

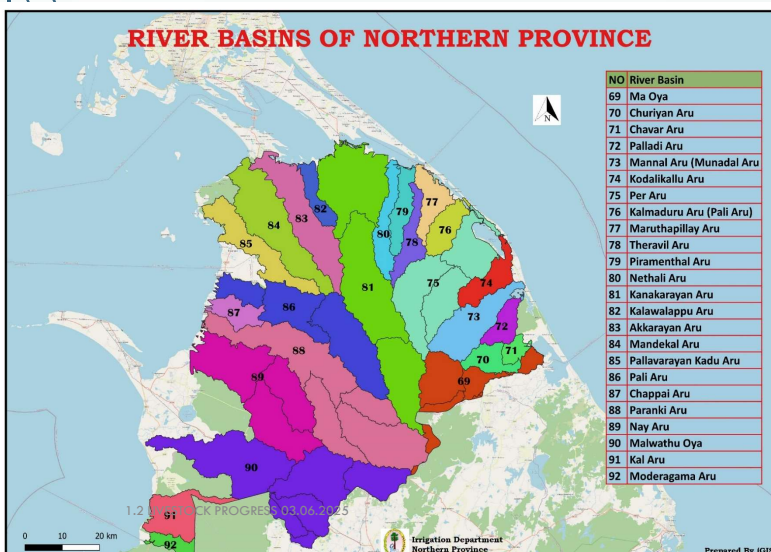

- 24 River basins of the 103

- 10 River basins are major which can be further enhanced.

(9 Provincial & 1 National Basins)

- 63 Major /medium schemes irrigating 63,675ha

Inter-Provincial Schemes -09

Provincial Schemes- 54

- 2,661 Minor tanks irrigating 31,398ha

COMPLETED PROJECTS

- Completed the feasibility study of River for Jaffna with assistance of Netharland Govt.
- Commencement of Alternative Drinking Water Supply (ADS) Project by Central Irrigation Dept. at Vadamarachchi Lagoon for source of Water Supply of Jaffna Peninsula
- Augmented Iranamadu scheme (from 131 MCM to 148 MCM) in order to increase the Yala cultivation by 20% of full extent
- Rehabilitated Thiruviaru Lift Irrigation schemes with Solar system (Net Plus connection) after 30 years.
- Augmented Muthuiyankaddu scheme in order to increase the capacity from 50.6 MCM to 59.2 MCM
- Augmented Vavunikulam scheme in order to increase the capacity from 43.54 MCM to 51.73 MCM

1.2 LIVESTOCK PROGRESS 03.06.2025

COMPLETED PROJECTS – IWWRMP – Kalmadu Head Works



Completed Bund and toe drain



Sluice and riprap

1.2 LIVESTOCK PROGRESS 03.06.2025

COMPLETED PROJECTS – JKWSSP – Iranamadu Head Works



Completed New radial Gates on LB side



Entrance of Iranamadu



Completed Bridge



Office Building at Mankulam

COMPLETED PROJECTS – IIDP Iranamadu Downstream



LB Main Canal




LB Main Canal Culvert



COMPLETED PROJECTS – THIRUVAIARU LIFTED IRRIGATION



COMPLETED PROJECTS – DSWRPP – MUTHTHUIYANKADDU TANK

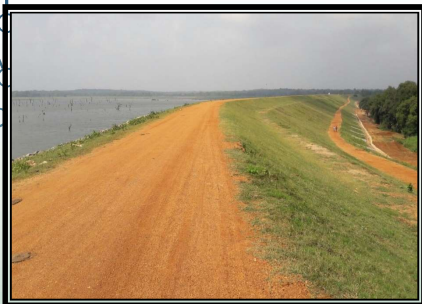

Muthaiyankaddu Bund - DSWRPP

Muthaiyankaddu Spill - DSWRPP

1.2 LIVESTOCK PROGRESS 03.06.2025

SECTORAL MEETING – 19.11.2024

COMPLETED PROJECTS – CARE – VAVNIKULAM TANK



REHABILITATION OF VAVUNIKULAM SCHEME HEAD WORKS

PROGRESS GOSL FUNDED WORKS 2025

1.2 LIVESTOCK PROGRESS 03.06.2025

OVERALL PROGRESS			
S. No	Source of Fund	No of Projects	Allocation Rs. (Mn)
GOSL Funding			
1	PSDG	37	594.000
2	CBG	06	39.650
3	RECURRENT	72	300.000
Sub Total		115	933.65
Foreign Funded Projects			
4	CISAP	33	1936.65
5	ASMP	07	272.35
6	IWWRMP	16	3567.11
7	IWWRMP – Re-Purposing	86	468.30
8	CResMPA	33	174.40
9	SARP	9	139.500
Sub Total		184	6558.31
Total			

OVERALL SUMMARY OF GOSL– 2025									
S. N	Source of Fund	Allocation (Mn)	Expenditure	No.of Activities	Estimate under preparation	Under Procurement	Awarde d	ongoing	Complete d
01	PSDG	594.00	3.602	37	04	08	09	14	01
02	CBG	39.65	-	06	-	-	05	01	-
03	Recurrent	300.00	8.676	72	07	12	21	31	01
Total		933.65	9.835	115	11	20	35	46	02

PSDG						
S.N	Name of Work	Allocation (Mn)	Location (District & Division)	Physical Progress %	Financial Progress (Mn)	Reason for non commencement
Kilinochchi Range						
01	Improvements Radial gates of Iranamadu Irrigation Scheme (Continu....)	4.997	Kilinochchi Karachchi	60%	-	
02	Improvements Activities to the Head work of Driaru Tank (Continu....)	2.869	Kilinochchi Karachchi	95%	0.366	Backfilling pending
03	Improvements Activities to the Head work of Kanagambikai Irrigation Scheme (Continu....)	4.385	Kilinochchi Karachchi	80%	-	
04	Improvement of Bund and spillway under Puthumurippu irrigation scheme (Continu....)	4.374	Kilinochchi Karachchi	50%	-	Delay due to water level in tank
05	Expand Solar Power System for Skanthapuram Lift Irrigation scheme(Continu....)	1.689	Kilinochchi Karachchi	100 %	0.995	

PSDG						
S.N	Name of Work	Allocation (Mn)	Location (District & Division)	Physical Progress %	Financial Progress (Mn)	Reason for non commencement
06	Improvement of Thondaimanaru barrage gates and other connected Components in Vadamarachchi Lagoon Scheme	15.000	Jaffna Point pedro	-	-	Water in Lagoon
07	Improvement to Piramanthararu kilinochchi East Division	55.000	Kilinochchi Kandawalai	-	-	Tender called
08	Replacing Rubber beadings for Balance Gates and fixing of dial indicators to Iranamadu Spill Gates	17.500	Kilinochchi Karachchi	-	-	Agreement signed
09	Improvement to Paranthan Main Canal and structures in LB at Kilinochchi East Division	12.749	Kilinochchi Karachchi	-	-	Start Date 10.07.2025
10	Improvement to Tank Bund Downstream under Iranamadu Scheme at Kilinochchi East Division	35.000	Kilinochchi Karachchi	25%	-	
11	Improvement of Kudamuruddy Tank Bund	20.000	Kilinochchi Poonakary	-	-	Delay due to water level in tank
12	Improvement Activities to LB Channel and Road under Kudamuruddy Scheme	15.000	Kilinochchi Poonakary	-	-	Retender

PSDG						
S.N	Name of Work	Allocation (Mn)	Location (District & Division)	Physical Progress %	Financial Progress (Mn)	Reason for non commencement
13	Improvement Activities to LB Channel and Road under Kariyalaingapaduwan Scheme	13.937	Kilinochchi Poonagary	-	-	Work commenced
14	Improvement of Spill way under Puthumurippu Irrigation Scheme	10.000	Kilinochchi Karachchi	-	-	Under evaluation
15	Improvement of FC 6 & FC 10 off D2 channel under Puthumurippu irrigation scheme	6.000	Kilinochchi Karachchi	-	-	Under evaluation
16	Improvement of FC 32 and FC 50 irrigation roads under Kariyalainagapaduwan irrigation scheme	6.000	Kilinochchi Poonagary	-	-	LOA
17	Construction of Conference hall cum Accounts branch at DDI office Kilinochchi	15.000	Kilinochchi Poonagary	7%	-	
	Sub Total	239.500			1.361	

1.2 LIVESTOCK PROGRESS 03.06.2025

PSDG						
S.N	Name of Work	Allocation (Mn)	Location (District & Division)	Physical Progress %	Financial Progress (Mn)	Reason for non commencement
Mullaitivu Range						
01	Improvement of Head works at Madawalaingan Tank in Muthuiyankaddu Division (Continu...)	19.137	Mullaitivu Maritimepattu	44%	-	-
02	Improvement of RB Canal Service Road in Vavunikkulam tank in Vavunikulam Division	10.000	Mullaitivu Thunukkai	-	-	Tender called
03	Improvement of LB Canal & Canal Road at Kalvilankulam in Vavunikulam Division	10.000	Mullaitivu Thunukkai	5%	-	Commenced
04	Improvements of Canal & Road at Vavunikulam Downstream area	5.000	Mullaitivu Manthai East	-	-	Tender called
05	Rehabilitation of Head works at Maruthamadu Tank in Muthuiyankaddu Division	40.000	Mullaitivu Puthukudiyiriupu	-	-	Water in tank
06	Rehabilitation of Head works of Kanukerny Tank in Muthuiyankaddu Division	25.000	Mullaitivu Maritimepattu	-	-	Bid Opened
07	Improvements to South Canal Road at Thannimurippu Scheme in Muthuiyankaddu Division	30.863	Mullaitivu Oddusuddan	-	-	Bid Opened

1.2 LIVESTOCK PROGRESS 03.06.2025

PSDG						
S.N	Name of Work	Allocation (Mn)	Location (District & Division)	Physical Progress %	Financial Progress (Mn)	Reason for non commencement
08	Rehabilitation of Lift Irrigation Scheme at Visuvamadu tank in Muthuiyankaddu Division(Continu....) .	92.000 (Special fund)	Mullaitivu Puthukudiyiriupu	-	-	Bids under evaluation
09	Improvement to South Canal Road from 6+500 m under Thannimurippu Tank, in Muththuiyankaddu Division	15.000	Mullaitivu Oddusuddan	-	-	Bids under evaluation
10	Reconstruction of Culvert in RB Access Road at Vithyapuram under Muththuiyankaddu Tank, in Muththuiyankaddu Division	7.000	Mullaitivu Oddusuddan	-	-	Bids under evaluation
	Sub Total	254.000				

1.2 LIVESTOCK PROGRESS 03.06.2025

PSDG						
S.N	Name of Work	Allocation (Mn)	Location (District & Division)	Physical Progress %	Financial Progress (Mn)	Reason for non commencement
Vavuniya Range						
01	Improvements of Tank Bund at Kombuvaiththakulam Irrigation Scheme (Continu...)	6.159	Vavuniya Vavuniya	50%	2.241	
02	Improvements to Nanchadichchapallam Anicut Irrigation Scheme	10.000	Vavuniya Vavuniya North	-	-	Ready to award
03	Improvements to Periyathampanai Irrigation Scheme.	5.000	Vavuniya Vengalacheddikulam	5%	-	Work commenced
04	Construction of Vavuniya Irrigation Engineer's Office (Balance work)	14.841	Vavuniya Vavuniya	-	-	LOI sent
		36.000				
05	Improvements of Kalmari Anicut, Diversion Canal and Koorai Tank Bund at Koorai Irrigation Scheme. (Continu...)	3.776	Mannar Manthai West	65%	-	
06	Improvements of Tank Bund at Koorai Irrigation Scheme.	16.000	Mannar Manthai West	5%	-	LOI sent

PSDG						
S.N	Name of Work	Allocation (Mn)	Location (District & Division)	Physical Progress %	Financial Progress (Mn)	Reason for non commencement
07	Improvements to Diversion Canal from Kalmari Anicut to Koorai Tank at Koorai Irrigation Scheme.	29.224	Mannar Manthai West	50%	-	
08	Improvements of Diversion Canal From Kalmari Anicut to Koorai Tank at Koorai Irrigation Scheme (Balance Work)	15.000	Mannar Manthai West	-	-	Work awarded
Northern Province						
01	Efficient Irrigation - Water management	0.250	Mullaitivu	-	-	Modules under Preparation
02	Maintenance of Irrigation Scheme in participatory Approach	0.250	Mullaitivu	-	-	Modules under Preparation
Grand Total		594.000			3.602	

1.2 LIVESTOCK PROGRESS 03.06.2025

CBG						
S.N	Name of Work	Allocation (Mn)	Location (District & Division)	Physical Progress %	Financial Progress (Mn)	Reason for non commencement
Kilinochchi Range						
01	Renovation of Skanthapuram - Kannagaipuram Joint Road (Continu.....)	17.650	Kilinochchi Karachchi	97%	Bill in hand 11.05 Mn	
02	Purchasing of Office equipment and furniture	1.000	Kilinochchi Karachchi	-	-	Purchasers order issued
Mullaitivu Range						
03	Purchasing of Office equipment's and furniture	2.000	Mullaitivu Oddusuddan			Purchasers order issued
Vavuniya Ranges						
04	New Construction of IE's Quarters at Pallamadu in Mannar	17.000	Mannar Manthai West			Tender called
05	Purchasing of Office equipment and furniture	1.000	Vavuniya Vavuniya			Purchasers order issued
Head office						
06	Purchasing of Office equipments and furniture	1.000	Mullaitivu Oddusuddan			Purchasers order issued
Total		39.650				

RECURRENT						
S.N	Name of Work	Allocation (Mn)	Location (District & Division)	Physical Progress %	Financial Progress (Mn)	Reason for non commencement
Kilinochchi Range - Tanks						
01	Purchasing Maintenance items , O & M Activities in Jaffna Division	1.000	Jaffna Jaffna	75%	0.512	
02	Improvement & Maintenance of SWE Schemes at Island areas	5.000	Jaffna Jaffna	-	-	Tender called
03	Improvement & Maintenance of SWE Schemes at sanganaï and karainagar areas	3.000	Jaffna Chankanai	-	-	Under evaluation
04	Improvement & Maintenance of Valukaiyaru scheme	7.000	Jaffna Tellipalai,Uduvil Chankanai, Sandilipay	-	-	Work started
05	O&M activities of Iranamadu Irrigation Scheme under Kilinochchi East Division.	2.000	Kilinochchi Karachchi	11%	-	
06	O&M activities of Irrigation Scheme under Kilinochchi East Division.	3.000	Kilinochchi Karachchi	13%	0.218	
1.2 LIVESTOCK PROGRESS 03.06.2025						

RECURRENT						
S.N	Name of Work	Allocation (Mn)	Location (District & Division)	Physical Progress %	Financial Progress (Mn)	Reason for non commencement
07	O&M activities of Kalmadu Scheme under Kilinochchi East Division.	2.000	Kilinochchi Karachchi	21%	0.393	
08	O&M activities of Piramantharu, Kanakampikai, Driaru Scheme under Kilinochchi East Division.	2.000	Kilinochchi Karachchi	7%	-	
09	Improvement & Maintenance to Iranamadu Sluice Area	2.000	Kilinochchi Karachchi	5%	-	Material arrived
10	Improvement & Maintenance to Iranamadu LB Channel Structures	7.000	Kilinochchi Karachchi	-	-	Bid under evaluation
11	Improvement & Maintenance to Canals in Lift Irrigation Scheme	2.000	Kilinochchi Karachchi	-	-	Agreement to be signed
1.2 LIVESTOCK PROGRESS 03.06.2025						

RECURRENT						
S.N	Name of Work	Allocation (Mn)	Location (District & Division)	Physical Progress %	Financial Progress (Mn)	Reason for non commencement
12	Improvement & Maintenance to D3 Main canal and RB3, LB2 off D3 in Iranamadu	4.000	Kilinochchi Karachchi	80%	1.995	
13	Improvement & Maintenance to Irrigation Structures at Kalmadu LB	3.000	Kilinochchi Kandawalai	-	-	Work start after Water issue
14	Improvement & Maintenance to Drainage Canal in Piramanthanaru	3.000	Kilinochchi Kandawalai	-	-	Tender called
15	Improvement & Maintenance, Providing Lightning to Kalmadu Scheme	2.000	Kilinochchi Kandawalai	-	-	Agreement to be signed
16	Improvement & Maintenance to FC Road in Iranamadu Scheme	3.000	Kilinochchi Kandawalai	-	-	Just started
17	Improvement & Maintenance of D1,D2,D3 channel, and Kannakaipuram OFC Scheme under Akkarayan Irrigation Scheme	20.000	Kilinochchi Karachchi	-	-	Tender called

12 LIVESTOCK PROGRESS 01.06.2015

RECURRENT						
S.N	Name of Work	Allocation (Mn)	Location (District & Division)	Physical Progress %	Financial Progress (Mn)	Reason for non commencement
18	Improvement & Maintenance of Skanthapuram Lift Irrigation Scheme under Akkarayan Irrigation Scheme	10.000	Kilinochchi Karachchi	-	-	Under evaluation
19	Improvement & Maintenance of D2 Channel under Puthumurippu Irrigation Scheme	10.000	Kilinochchi Karachchi	-	-	Delay due to water issue
20	Improvement & Maintenance Activities to FCs & Channel Roads under Kariyalainagapaduwan Irrigation Scheme	9.000	Kilinochchi Poonagari	7%	-	
21	Improvement & Maintenance Activities to FCs & Channel Roads under Akkarayan Irrigation Scheme	7.500	Kilinochchi Karachchi	-	-	Just started
22	Purchasing for O&M Activities of Irrigation Scheme under Kilinochchi west Division	2.000	Kilinochchi Karachchi	7%	-	
23	O&M Activities of Irrigation Scheme under Kilinochchi west Division	1.500	Kilinochchi Karachchi	10%	-	

RECURRENT						
S.N	Name of Work	Allocation (Mn)	Location (District & Division)	Physical Progress %	Financial Progress (Mn)	Reason for non commencement
Kilinochchi Range - Buildings						
24	Improvement & Maintenance to Office Building, Quarters & Lightning Room at Kalmadu	2.000	Kilinochchi Kandawalai	55%	-	
25	Improvement & Maintenance of Office Building & Quarters	2.000	Kilinochchi Karachchi	88%	1.500	
26	Improvement & Maintenance of Deputy Director of Irrigation's Office Building in kilinochchi Range.	2.000	Kilinochchi Karachchi	10%	-	
27	Improvement & Maintenance of Irrigation Engineer's Office & HRC Building's & other Land	1.000	Jaffna Point Pedro	70%	0.365	
28	Renovation of Skanthapuram – Kannagaipuram Joint Road (Phase-II)	1.5000		40%		
	Total	123.000			4.983	
1.2 LIVESTOCK PROGRESS 03.06.2025						

RECURRENT						
S.N	Name of Work	Allocation (Mn)	Location (District & Division)	Physical Progress %	Financial Progress (Mn)	Reason for non commencement
Mullaitivu District						
1	Improvement & Maintenance to Spillway at Muththuyankaddu Tank in Muthuyankaddu Division	5.000	Mullaitivu Oddusuddan	-	-	Tender called
2	Attending the Emergency work & General Maintenance & Purchasing of personal protectivity items in Muthuyankaddu Division	2.000	Mullaitivu Oddusuddan	-	-	Allocated for emergency work
3	Improvement & Maintenance of Electro - Mechanical Work at Thannimurippu Tank in Muthuyankaddu Division	1.000	Mullaitivu Oddusuddan	-	-	Water in Tank
4	Improvement & Maintenance of Electro - Mechanical Work at Muththuyankaddu Tank in Muthuyankaddu Division	3.000	Mullaitivu Oddusuddan	-	-	Water in Tank
5	Improvement & Maintenance of Access Road at Visuwamadu Tank in Muthuyankaddu Division	1.250	Mullaitivu Puthukudiyiruppu	-	-	Estimate Prepared (Allocation revised)
1.2 LIVESTOCK PROGRESS 03.06.2025						

RECURRENT						
S.N	Name of Work	Allocation (Mn)	Location (District & Division)	Physical Progress %	Financial Progress (Mn)	Reason for non commencement
6	Clearing, Desilting & Maintenance of RB Main Canal of Muthuiyankaddu Tank in Muthuiyankaddu Division	4.000	Mullaitivu Oddusuddan	-	-	Water issue
7	Clearing, Desilting & Maintenance of LB Main Canal of Muthuiyankaddu Tank in Muthuiyankaddu Division	1.000	Mullaitivu Oddusuddan	-	-	Water issue
8	Improvement & Maintenance of LB Canal & Agriculture Road at Madawalasingan Tank in Muthuiyankaddu Division	5.000	Mullaitivu Maritimepattu	-	-	Tender called
9	Improvement & Maintenance to LB off Track 11 & 12 Canal lining and Agriculture Road at Thannimurippu Tank in Muthuiyankaddu Division	9.250	Mullaitivu Oddusuddan	-	-	Estimate Prepared (Allocation revised)
10	Improvement & Maintenance to Canal lining and Agriculture Road at Maruthamadu Tank in Muthuiyankaddu Division	7.000	Mullaitivu Puthukudiyiruppu	-	-	Water issue

RECURRENT						
S.N	Name of Work	Allocation (Mn)	Location (District & Division)	Physical Progress %	Financial Progress (Mn)	Reason for non commencement
12	Improvement & Maintenance of Headworks & spill tail canal at Theniyankulam in Vavunikulam Division	5.000	Mullaitivu Thunukkai	-	-	Tender called
13	Improvement & Maintenance of Headworks at Vavunikulam Tank in Vavunikulam Division	10.000	Mullaitivu Thunukkai	-	-	Water in Tank
14	Attending the Emergency work & General Maintenance & Purchasing of personal productivity items in Vavunikulam Division	3.000	Mullaitivu Thunukkai	5%	-	
15	Maintenance & Renovation of FC 12 of RB main Canal at Theniyankulam in Vavunikulam Division	3.000	Mullaitivu Thunukkai	-	-	Commenced
16	Improvement & Maintenance of 4th canal off RB Main Canal at Kollavilankulam in Vavunikulam Division	3.000	Mullaitivu Manthai East	-	-	Water issue

1.2 LIVESTOCK PROGRESS 03.06.2025

RECURRENT						
S.N	Name of Work	Allocation (Mn)	Location (District & Division)	Physical Progress %	Financial Progress (Mn)	Reason for non commencement
17	Improvement & Maintenance of Canal at Panankamam Tank in Vavunikulam Division	2.000	Mullaitivu Manthai East	-	-	Commenced
18	Improvement & Maintenance to RB Main Canal Agriculture Road (2 km) at Therankandal in Vavunikulam Division	8.000	Mullaitivu Thunukkai	-	-	Commenced
19	Improvement & Maintenance to DC-12 -Canal lining and Agriculture Road in RB at Vavunikulam Tank in Vavunikulam Division	9.000	Mullaitivu Thunukkai	-	-	Tender called
21	Improvement & Maintenance of IE Office & quarters in Vavunikulam Division	2.500	Mullaitivu Thunukkai	-	-	Sanctioned
22	Improvement & Maintenance to DDI'S Office & Quarters in Mullaitivu Range	1.500	Mullaitivu Thunukkai	-	-	Sanctioned
23	Improvement & Maintenance to Madawalasingan & Kanukerny Quarters in Muthuyankaddu Division	2.000	Mullaitivu Maritimpeattu	-	-	Work just commenced
	Improvement of LB of DC-3 Cannel at Vavunikulam Tank in Vavunikulam Division	1.000	Mullaitivu Manthai East			New work
	Total	101.00				

RECURRENT						
S.N	Name of Work	Allocation (Mn)	Location (District & Division)	Physical Progress %	Financial Progress (Mn)	Reason for non commencement
Head Office						
01	Emergency works to mitigate flood damages during the Monsoon rainy Season	10.000	Mullaitivu Oddusuddan	-	-	Reserved for emergency work
02	Improvement & Maintenance to Head office Building.	5.000	Mullaitivu Oddusuddan	15%	0.603	
	Total	15.000			0.603	

RECURRENT						
S.N	Name of Work	Allocation (Mn)	Location (District & Division)	Physical Progress %	Financial Progress (Mn)	Reason for non commencement
Vavuniya District						
01	Maintenance & Improvement Works to Malikai tank, Chemamadu tank & Nampankulam Irrigation Schemes.	5.500	Vavuniya Vavuniya	-	-	Tender Called
02	Maintenance & Improvement Works to Vavuniya tank, Maharambaikulam & Moonayamadu tank Irrigation Schemes.	7.000	Vavuniya Vavuniya	-	-	Tender Called
03	Maintenance & Improvement Works to Kalmadu Tank & Pampaimadu Tank Irrigation Scheme.	6.000	Vavuniya Vavuniya	-	-	LOI sent
04	Maintenance & Improvement Works to Madukanda Tank & Mamaduwa Tank Irrigation Schemes.	5.000	Vavuniya South	-	-	Work awarded

RECURRENT						
S.N	Name of Work	Allocation (Mn)	Location (District & Division)	Physical Progress %	Financial Progress (Mn)	Reason for non commencement
05	Maintenance & Improvement Works to Kombuvaithakulam Irrigation Schemes.	2.000	Vavuniya Vavuniya	30%	-	
06	General Maintenance works of Tanks in Vavuniya & Cheddikulam Division including Purchasing of Tank Maintenance items	3.500	Vavuniya Vavuniya	20%	-	
07	Maintenance & Improvements of Office & Quarters Buildings in Vavuniya & Cheddikulam Division.	5.000	Vavuniya Vavuniya	-	1.138	
08	Maintenance & Renovation of Fence in Quarters buildings in Vavuniya & Cheddikulam Division including purchasing of Building Maintenance items	1.500	Vavuniya Vavuniya	100%	0.626	
09	Maintenance & Improvements of Office & Quarters Buildings in Vavuniya & Cheddikulam Division including Purchasing of Building Maintenance items	2.000	Vavuniya Vavuniya	90%	1.326	

RECURRENT						
S.N	Name of Work	Allocation (Mn)	Location (District & Division)	Physical Progress %	Financial Progress (Mn)	Reason for non commencement
Mannar District						
10	Maintenance & Improvement Works to Mullikulam Irrigation Scheme	3.000	Mannar Madhu	-	-	Agreement signed
11	Maintenance & Improvement Works to Kalmari Anicut and Diversion Canal at Koorai Tank Irrigation Scheme	3.500	Mannar Manthai West	-	-	Agreement signed
12	Maintenance & Improvement Works to Paliyaru Anicut Access Road and Control Structure at Adampankulam Irrigation Scheme	3.000	Mannar Manthai West	-	-	Agreement signed
13	Maintenance & Improvement Works to Periyapandivirichan Tank & Thadchanamaruthamadu Tank Irrigation Scheme	5.500	Mannar Madhu	-	-	LOI sent
14	Maintenance & Improvement Works to Periyamadu Tank & Welimaruthamadu Tank Irrigation Scheme	4.000	Mannar Manthai West	5%	-	
15	General Maintenance works of Tanks in Mannar Division including Purchasing of Tank Maintenance items	1.000	Mannar Manthai West	3%	-	

RECURRENT						
S.N	Name of Work	Allocation (Mn)	Location (District & Division)	Physical Progress %	Financial Progress (Mn)	Reason for non commencement
Mannar District						
16	Maintenance & Improvements of Office & Quarters Buildings in Mannar Division.	3.000	Mannar Manthai west	5%	-	
17	Maintenance & Improvements of Office & Quarters Buildings in Mannar Division including Purchasing of Building Maintenance items	0.500	Mannar Manthai west	-	-	Estimate Under Preparation
Sub Total		61.000			3.090	
Grand Total		300.000			8.676	

1.2 LIVESTOCK PROGRESS 03.06.2025

PHOTOS

Maintenance & Improvement Works to Kombuvaihakulam Irrigation Schemes- Recurrent



Improvement to Tank Bund Downstream under Iranamadu Scheme at Kilinochchi East Division - PSDG



Quarters Repair – Kilinochchi Recurrent



Improvements to Diversion Canal from Kalmari Anicut to Koorai Tank at Koorai Irrigation Scheme.- PSDG



Improvements to Periyathampanai Irrigation Scheme - PSDG



Maintenance & Renovation of Fence in Quarters buildings in Vavuniya & Cheddikulam Division including purchasing of Building Maintenance items- Recurrent



PHOTOS

Improvements of Kalmari Anicut, Diversion Canal and Koorai Tank Bund at Koorai Irrigation Scheme. (Continu...) PSDG



Renovation of Skanthapuram - Kannagaipuram Joint Road (Continu.....) - CBG



PROGRESS FOREIGN FUNDED WORKS 2024 - 2025

1.2 LIVESTOCK PROGRESS 03.06.2025

FOREIGN FUNDED PROJECTS

- **CSIAP**
- **ASMP**
- **IWWRMP**
- **IWWRMP (Re – Purposing)**
- **CResMPA**
- **SARP**

1.2 LIVESTOCK PROGRESS 03.06.2025

OVERALL SUMMARY OF Foreign Funded projects

S.N	Source of Fund	Allocation (Mn)	Expenditure	No.of Activities	Estimate under preparation	Under Procurement	Awarde d	ongoing	Complete d
01	CSIAP	1936.65	745.394	33	-	-	-	12	21
02	ASMP	272.35	144.65	07	-	-	-	04	03
03	IWWRMP	3567.11	1124.14	16	04	02	02	01	07
04	IWWRMP-Repurposing	468.30	305.764	86	-	04	-	01	81
05	CResMPA	174.40	40.232	33	-	-	-	17	16
06	SARP	139.500	12.720	9	-	05	01	03	-
Total		6558.31	2362.900	184	04	11	03	38	128

Climate Smart Irrigated Agriculture Project (CSIAP)

S.N	District	No of Works	Allocation (Mn)	Expenditure (Mn)	Remarks
01	Mullaitivu	23	1230.99	305.03	Completed Projects (14) Terminated Project (01) Commenced (08)
02	Kilinochchi	10	705.66	440.364	Completed (06) Ongoing Projects (04)
Total		33	1936.65	745.394	

Climate Smart Irrigated Agriculture Project (CSIAP)

NOS	ACTIVITES	Contract Amount including VAT	Physical Progress	Expenditure	REMARKS
1	Improvement of Semmankuntru Tank	115.37	90%	55.05	Work in progress
2	Construction of Head works & canal system of Thevankaddu kulam	114.55	78%	46.99	
3	Construction of Head works & Vanneri kulam	114.554	68%	45.66	
4	Rehabilitation of Downstream works under Vanneri Irrigation Scheme	100.804	95%	51.542	
Total		445.278		199.242	

1.2 LIVESTOCK PROGRESS 03.06.2025

Climate Smart Irrigated Agriculture Project (CSIAP)

NOS	ACTIVITES	Contract Amount including VAT	Expenditure (Rs. In MN)	Physical Progress	REMARKS
1	Rehabilitation of Palayamurukandy kulam Tank	59.62			Awarded (delay due to the water in tank & Water issue)
2	Rehabilitation of Kodaikaddiyakulam Tank	56.64			
3	Rehabilitation of Iyankankulam Tank	66.88			
4	Rehabilitation of Ampalaperumalkulam Tank	62.54			

1.2 LIVESTOCK PROGRESS 03.06.2025

Climate Smart Irrigated Agriculture Project (CSIAP)					
S.N	ACTIVITES	Contract Amount including VAT	Physical Progress	Financial Progress	REMARKS
5	Rehabilitation of Ampalaperumalkulam Downstream in Vavunikulam Division	85.67			Commenced
6	Rehabilitation of Palayamurukandy Downstream in Vavunikulam Division (LK-MOA-468996-CW-RFB-NP)	78.65			
7	Rehabilitation of Kodaikaddiyakulam Downstream in Vavunikulam Division	78.83			
8	Rehabilitation of Iyankulam Downstream in Vavunikulam Division	84.77			
	Total	573.6			

1.2 LIVESTOCK PROGRESS 03.06.2025

Agriculture Sector Modernization Projects (ASMP)					
S.N	District	No of Works	Allocation (Mn)	Expenditure (Mn)	Remarks
01	Mullaitivu	03	108.35	54.52	Completed Projects
02	Kilinochchi	01	17.76	8.30	Completed Projects
03	Vavuniya	02	54.04	23.79	Completed Projects
04	Jaffna	01	92.20	58.04	Completed Projects
	Total	07	272.35	144.65	

1.2 LIVESTOCK PROGRESS 03.06.2025

Integrated Watershed & Water Resource Management Project (IWWRMP) – Phase 1

S.N	District	No of Works	Allocation (Mn)	Expenditure (Mn)	Remarks
01	Mullaitivu	04	590.4	341.02	Completed (04)
02	Kilinochchi	03	859.56	804.37	Completed (03)
Total		07	1450.01	1124.14	

1.2 LIVESTOCK PROGRESS 03.06.2025

Integrated Watershed & Water Resource Management Project (IWWRMP) – Phase 1

S.No	Name of The Works	Contract Amount	Physical Progress%	Financial Progress (Mn)
01	Rehabilitation of Kalmadu scheme	778.23	100%	737.55
02	Rehabilitation of Piramanthalaru kulam	32.52	100%	26.66
03	Rehabilitation of Downstream infrastructure of kanakambikai kulam	48.81	100%	40.16
04	Rehabilitation of Muththuyankaddu (Package 1)	106.49	100%	51.07
05	Rehabilitation of Muththuyankaddu (package 3)	135.69	100%	108.70
06	Rehabilitation of Muththuyankaddu (Package 4)	166.64	100%	106.35
07	Rehabilitation of Muththuyankaddu (package 5)	170.72	100%	53.65
TOTAL		1439.10		1124.14

1.2 LIVESTOCK PROGRESS 03.06.2025

Integrated Watershed & Water Resource Management Project (IWRMP) – Phase ii			
S.No	Name of Works	Allocation in (Mn)	Status
1	Rehabilitation of Maruthankulam tank	200.00	Work in Progress (5%)
2	Rehabilitation of Niththakaikulam	225.00	Waiting for Award (Bid invited on 01.09.2024, closed on 02.10.2024)
3	Rehabilitation of Kariyalainagapaduwan	447.50	Bid Invited on 16.03.2025 TEC Report submitted
4	Rehabilitation of Spill of Kalmadu Tank	213.60	Revised estimate(28.05.2025) and draft bidding document submitted (29.05.2025)
5	Rehabilitation of Periyamadu	300.00	Waiting for bid invitation
6	Rehabilitation of Mallavi Tank	120.00	Revised estimate(28.05.2025) and draft bidding document submitted(29.05.2025)
7	Rehabilitation of Welimaruthamadu Tank Downstream	46.00	Ready to award
8	Rehabilitation of Thannimurippu Tank	550.00	Revised estimate and draft bidding document submitted(28.05.2025)
9	Institutional Development of Irrigation Department, NP	15.00	Estimates submitted(24.03.2025)
	Total	2,117.10	

Integrated Watershed & Water Resource Management Project (IWRMP) – Phase ii					
S.N	District	No of Works	Allocation (Mn)	Expenditure (Mn)	Remarks
01	Mullaitivu	04	1095.00	-	01 Works ready to award 01 On going 02 Revised estimate and draft bidding document submitted
02	Kilinochchi	02	661.10	-	01 Under evaluation 01 Revised estimate and draft bidding document submitted
03	Mannar	02	346.00	-	01 Work waiting for bid Invitation 01 Ready to award
04	Province	01	15.00	-	Estimate submitted
	Total	09	2117.10		

Integrated Watershed & Water Resource Management Project (IWWRMP - RePurposing)

S.N	District	No of Works	Allocation (Mn)	Expenditure (Mn)	Remarks
01	Mullaitivu	08	41.70	34.430	Fully Completed
02	Kilinochchi	17	83.30	61.911	Fully Completed
03	Vavuniya	17	83.30	66.993	Fully Completed
04	Mannar	13	83.30	44.944	11 Completed Projects 02 Under Procurement
05	Jaffna	31	176.70	97.535	28 Completed Projects 03 Projects (02 Works Under evaluation, 01 Ongoing)
Total		86	468.30	305.764	

Climate Resilience Multi Phase Approach (CResMPA)

S.N	Range	No of Works	Allocation (Mn)	Expenditure (Mn)	Remarks
01	Mullaitivu	03	24.75	3.519	01 Completed Projects 02 Ongoing Projects
02	Kilinochchi	07	52	10.249	04 Completed Projects 03 Ongoing Projects
03	Vavuniya	11	22.40	7.748	07 Completed Projects 04 Ongoing Projects
04	Mannar	07	30	15.219	03 Completed Projects 04 Ongoing Projects
05	Jaffna	05	50	3.497	01 Completed Projects 04 Ongoing Projects
Total		33	174.40	40.232	

Smallholder Agribusiness and Resilience Project (SARP)

S.N	Range	No of Works	Allocation (Mn)	Expenditure (Mn)	Remarks
01	Vavuniya	09	139.500	12.620	05 Bid Called 01 Work awarded 03 work ongoing
	Total	09	139.500	12.620	

1.2 LIVESTOCK PROGRESS 03.06.2025

Smallholder Agribusiness and Resilience Project (SARP)

No.	Description of Work	Allocation (Rs. in Mn)	Expenditure (Rs. in Mn)	Phy. Progress %	Remarks
1	Rehabilitation of Koolankulam	15.500	3.17	40%	Work in progress
2	Rehabilitation of Kollankulam	15.500	2.75		Work awarded
3	Rehabilitation of Udaiyarkulam	15.500	3.23	15%	Work in progress
4	Rehabilitation of Kalliyamurippu	15.500	3.47	5%	Work in progress
		62.000	12.620		

No.	Description of Work	Allocation (Rs. in Mn)	Expenditure (Rs. in Mn)	Phy. Progress %	Achievement during Last Week %	Remarks
1	Rehabilitation of Periyapuliyalankulam	15.500				Bid Called.
2	Rehabilitation of Mayilmuddaiiddakulam	15.500				
3	Rehabilitation of Cheddikulam	15.500				
4	Rehabilitation of Olumadu	15.500				
5	Rehabilitation of Kurinchakulam	15.500				
		77.500				

1.2 LIVESTOCK PROGRESS 03.06.2025

ISSUES

1.2 LIVESTOCK PROGRESS 03.06.2025

OVERALL PROGRESS			
S. No	Source of Fund	No of Projects	Allocation Rs. (Mn)
GOSL Funding			
1	PSDG	37	594.000
2	CBG	06	39.650
3	RECURRENT	72	300.000
Sub Total		115	933.65
Foreign Funded Projects			
4	CISAP	33	1936.65
5	ASMP	07	272.35
6	IWWRMP	16	3567.11
7	IWWRMP – Re-Purposing	86	468.30
8	CResMPA	33	174.40
9	SARP	9	139.500
Sub Total		184	6558.31
Total			

1. Cadre Issues

- **Technical Staffs(Engineers/Technical Officers/ Draughtsman)**
- **Maintenance Labour**

Designation	Approved Cadre	Present Cadre
Engineer	19	14
Deputy Director	3	3
Technical Officer(Civil)	82	63
Technical Officer (Special)	8	2
Technical Officer(Electrical)	2	0
Draughtman	17	12
Draughtsman(Special)	3	0
Soil Testers	8	5
Soil Testers (Special)	1	0
ML	186	73

2. Land Ownership / Encroachment Issues(We're unable to take legal actions)



THANK YOU

1.2 LIVESTOCK PROGRESS 03.06.2025
